AGILE PROJECT MANAGEMENT

Introduction to AGILE – The Basic 101

Nurul Haszeli Ahmad

4th December 2015

CONTENTS

1 Project Management

2 AGILE

3 AGILE Project Management Process Flow

4 Transition from Traditional to Agile

5 Applying Agile

6 Q & A


1 Project Management – Why and What








"Project Management is an art of managing and ensuring the RESOURCES is utilize efficiently, within the TIME allocated, to deliver highest QUALITY of deliverables"
– Ir Mohd Haizad Hussin, MD of Matrix Power Network

1 Project Management – The Traditional Method

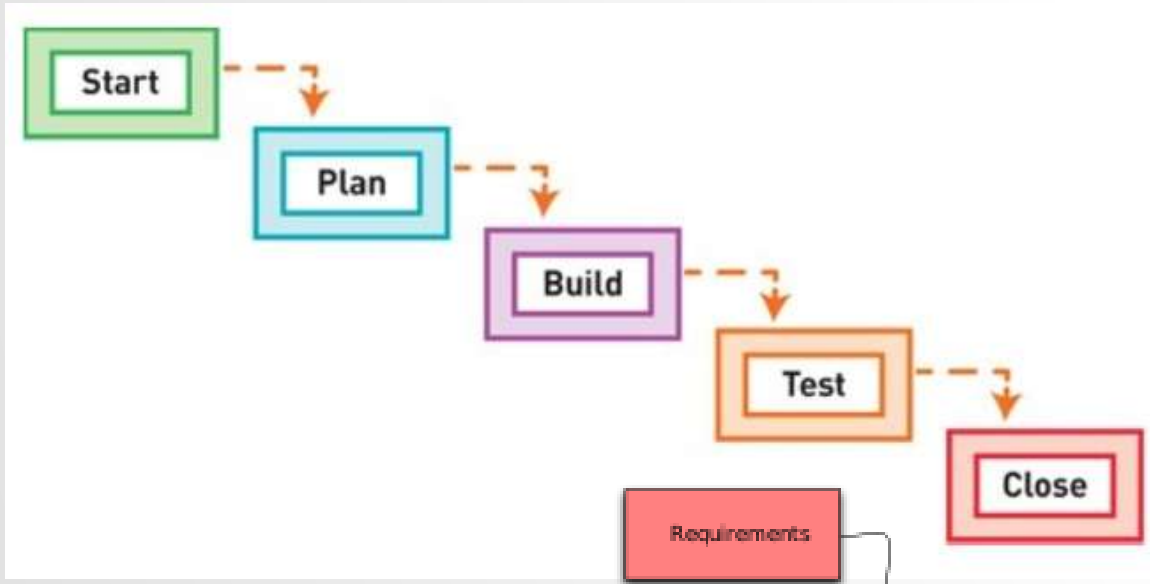


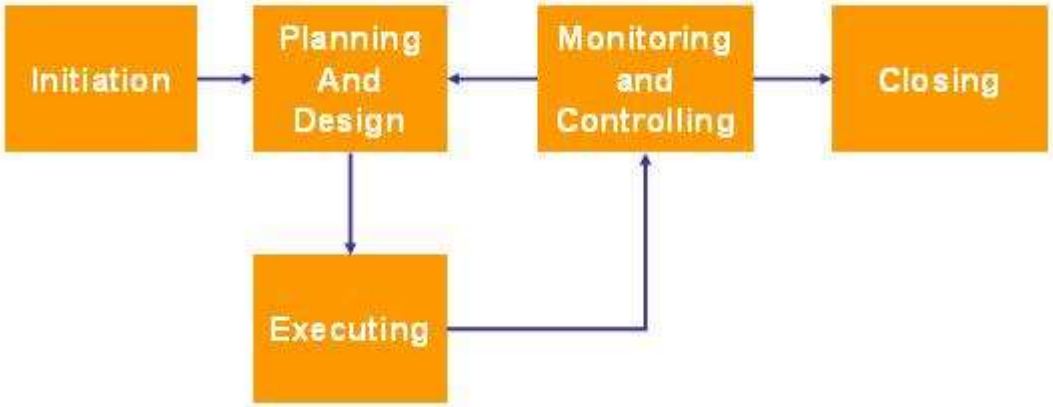

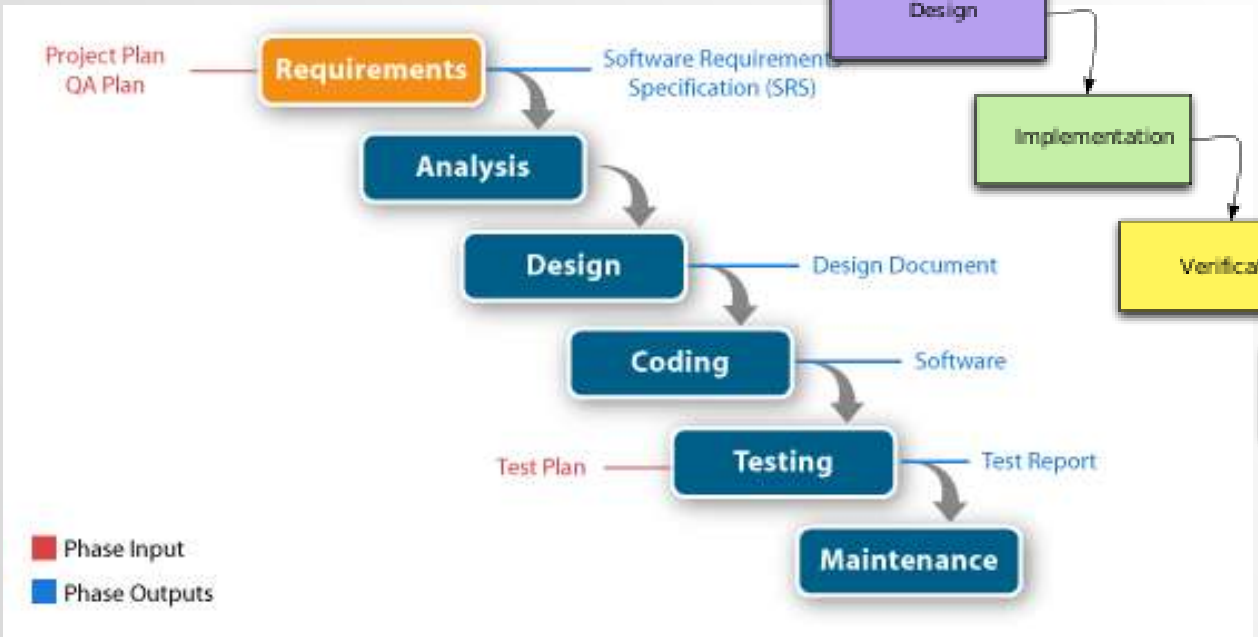

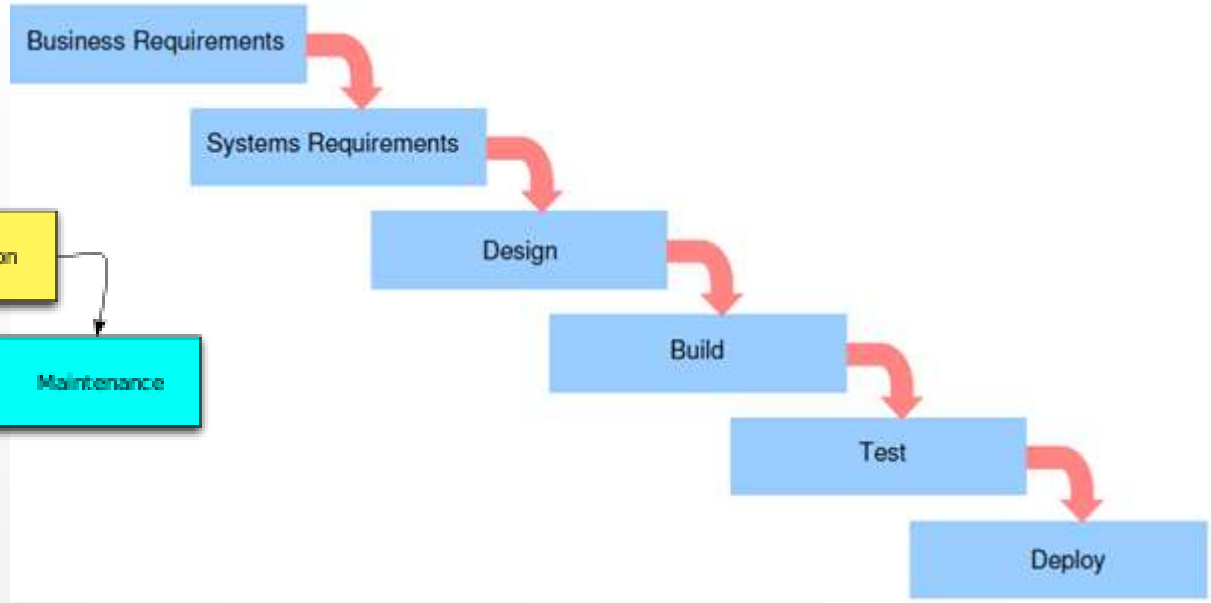


1 Project Management – The Not So Traditional Method

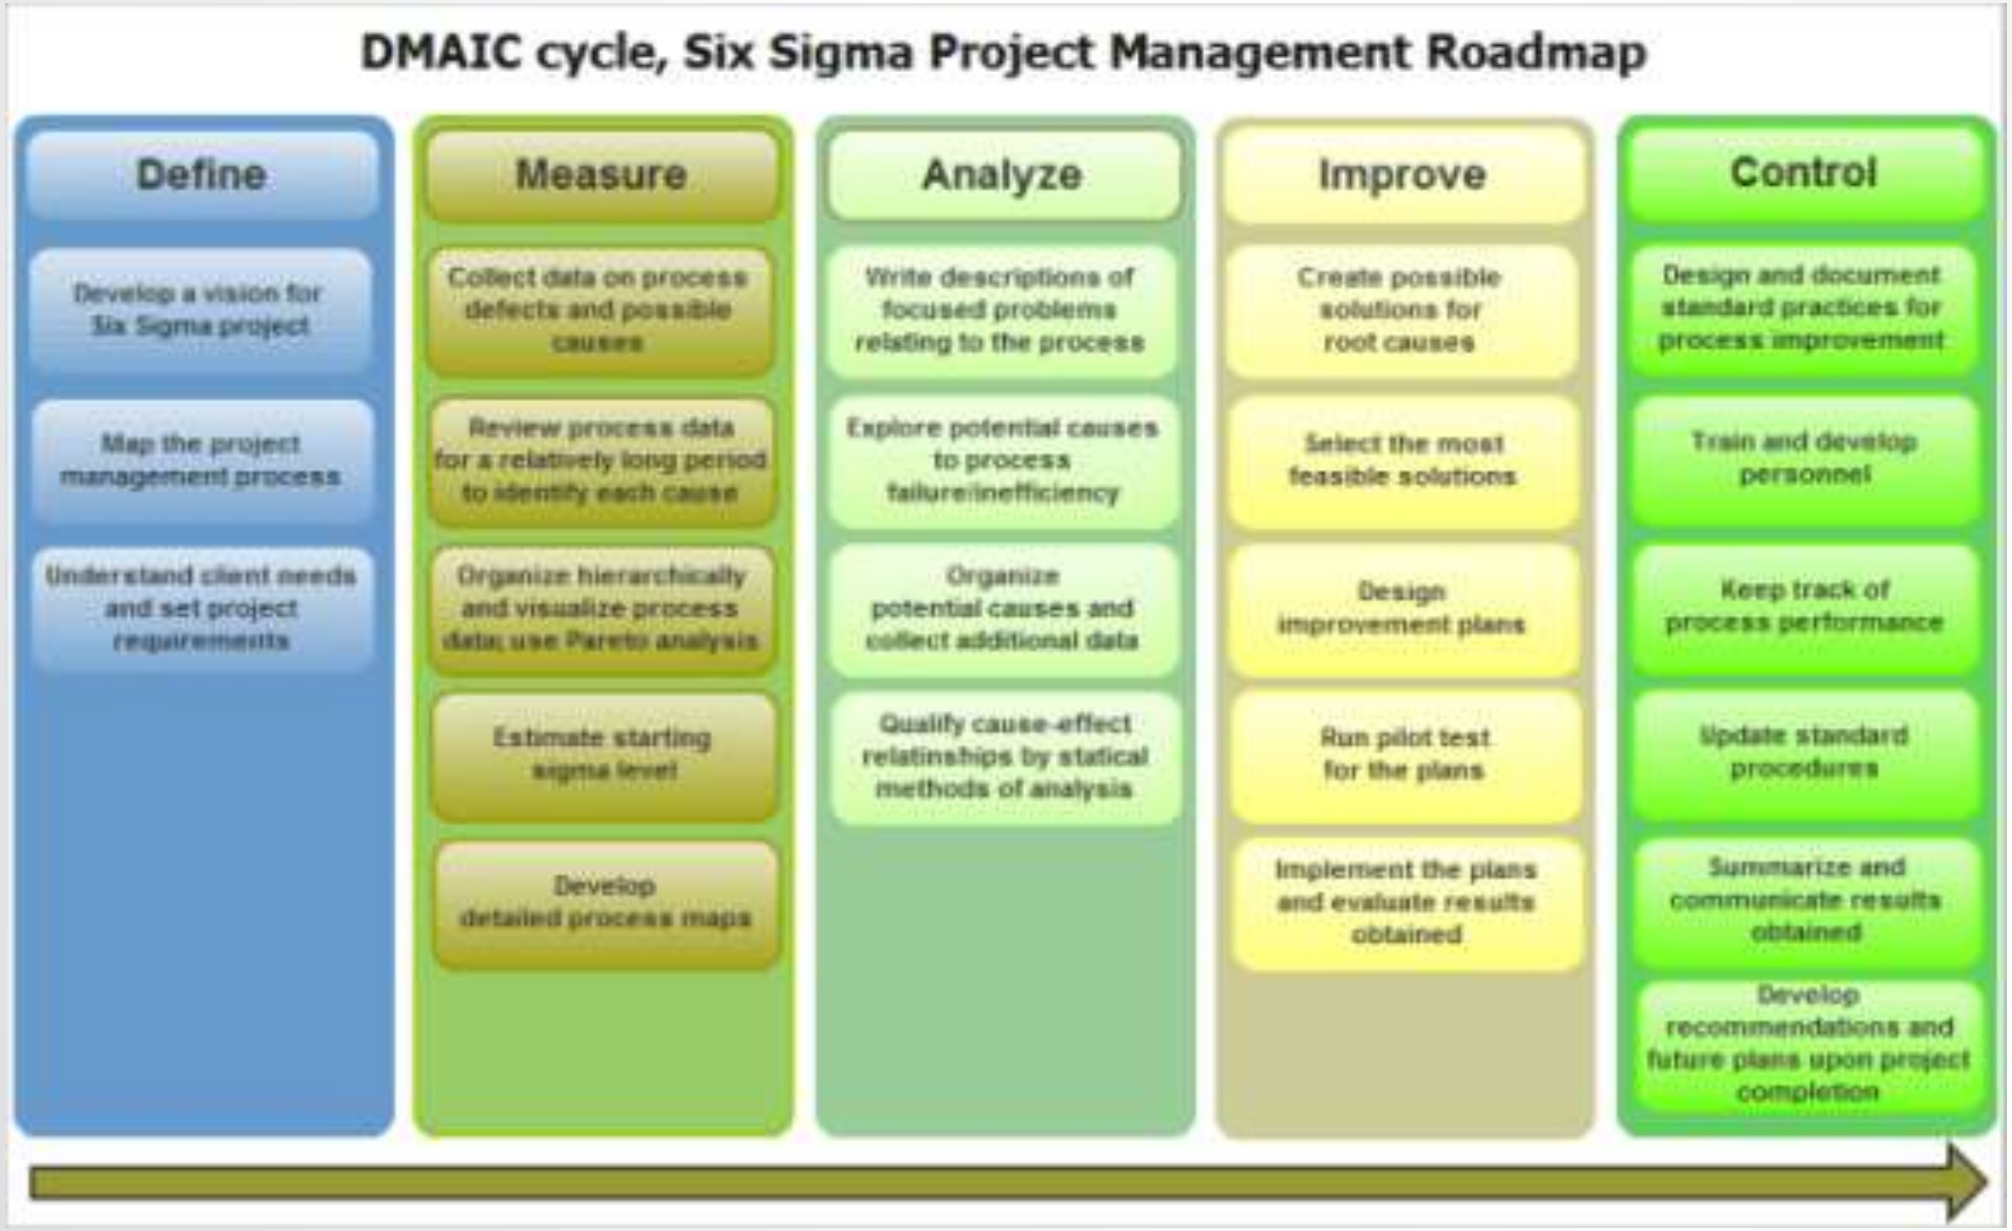


Source: Jack Grabovski (MyMG) – Lean Thinking Project Management in Six Sigma and Agile Models (http://www.mymanagementguide.com/lean-thinking-project-management-six-sigma-agile-models/)

1 Project Management – The Traditional Method

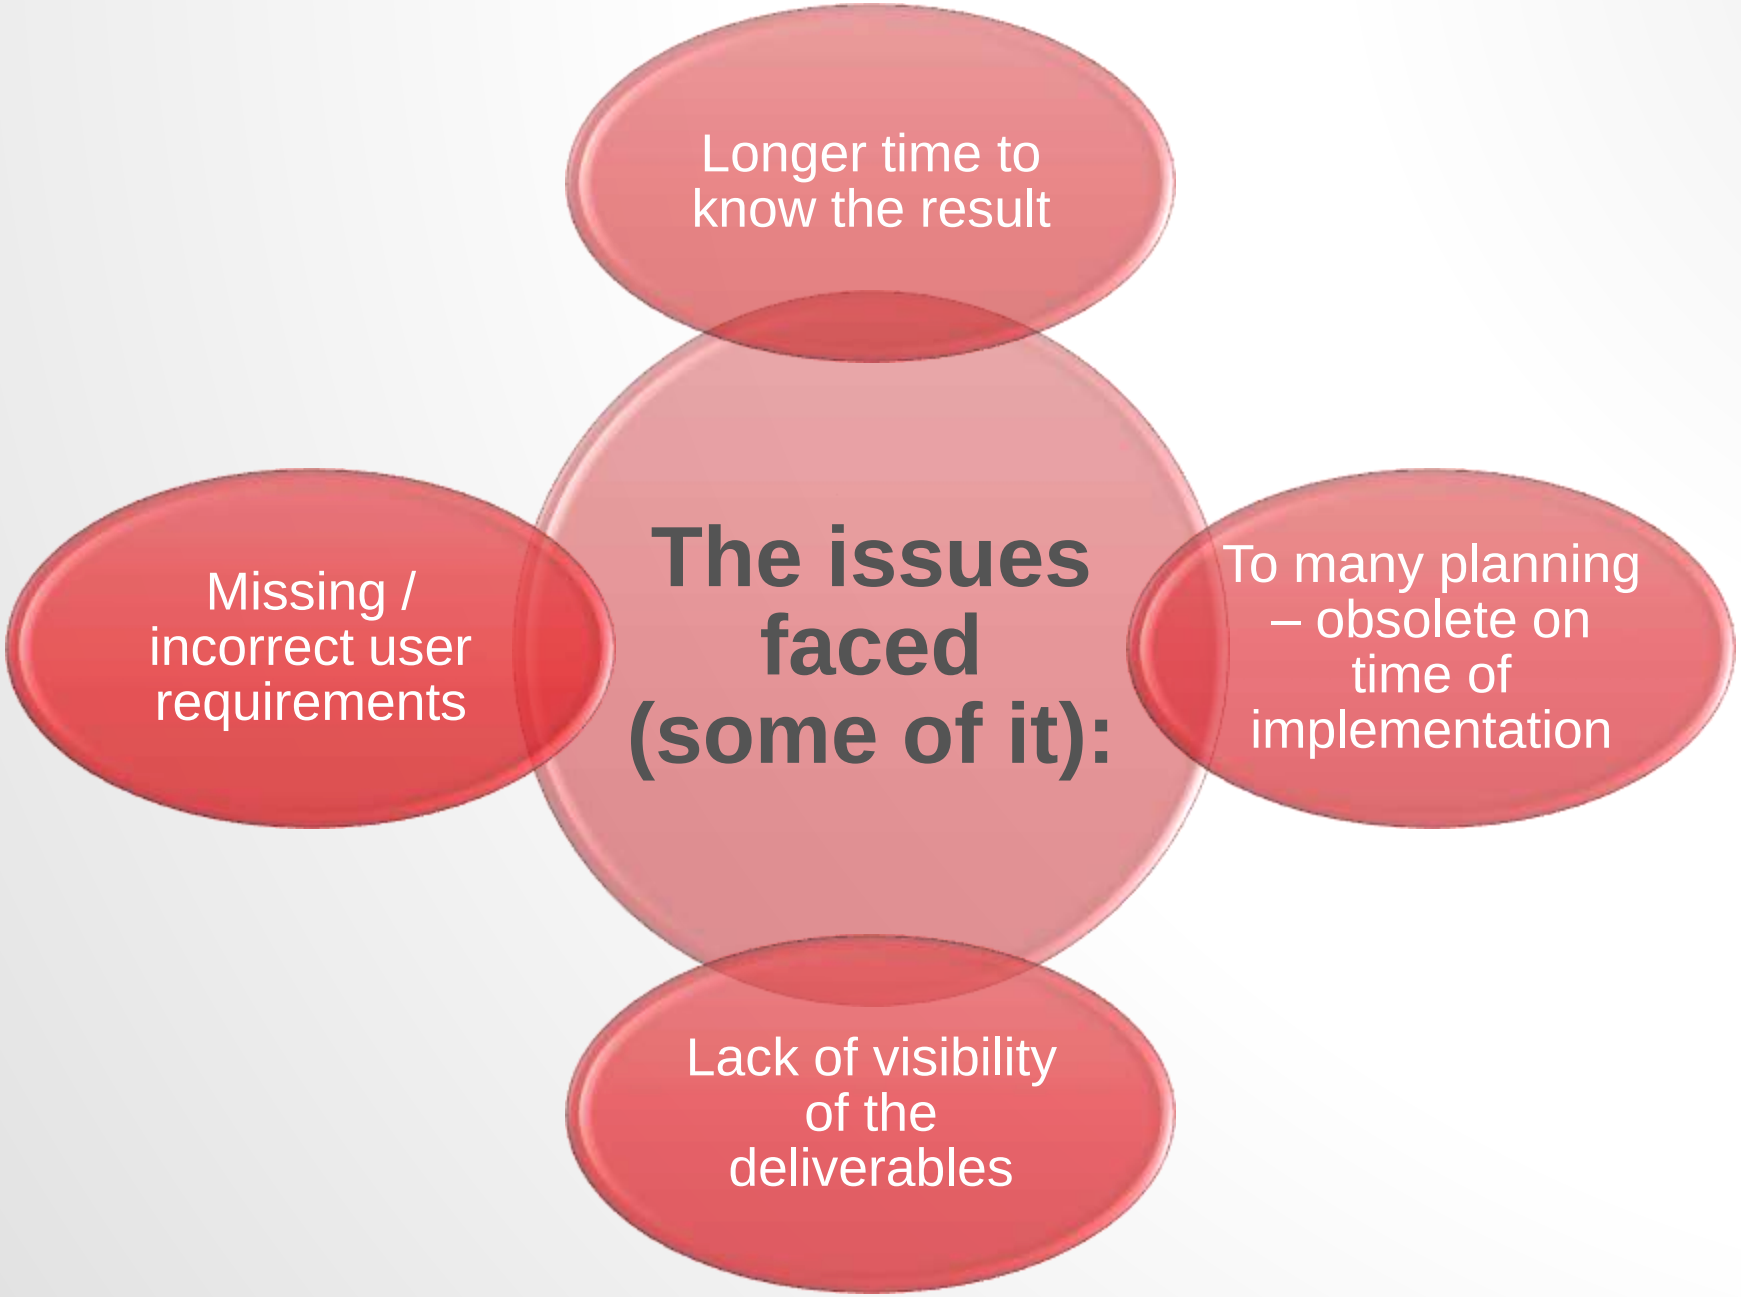


1 Project Management – The Traditional Method

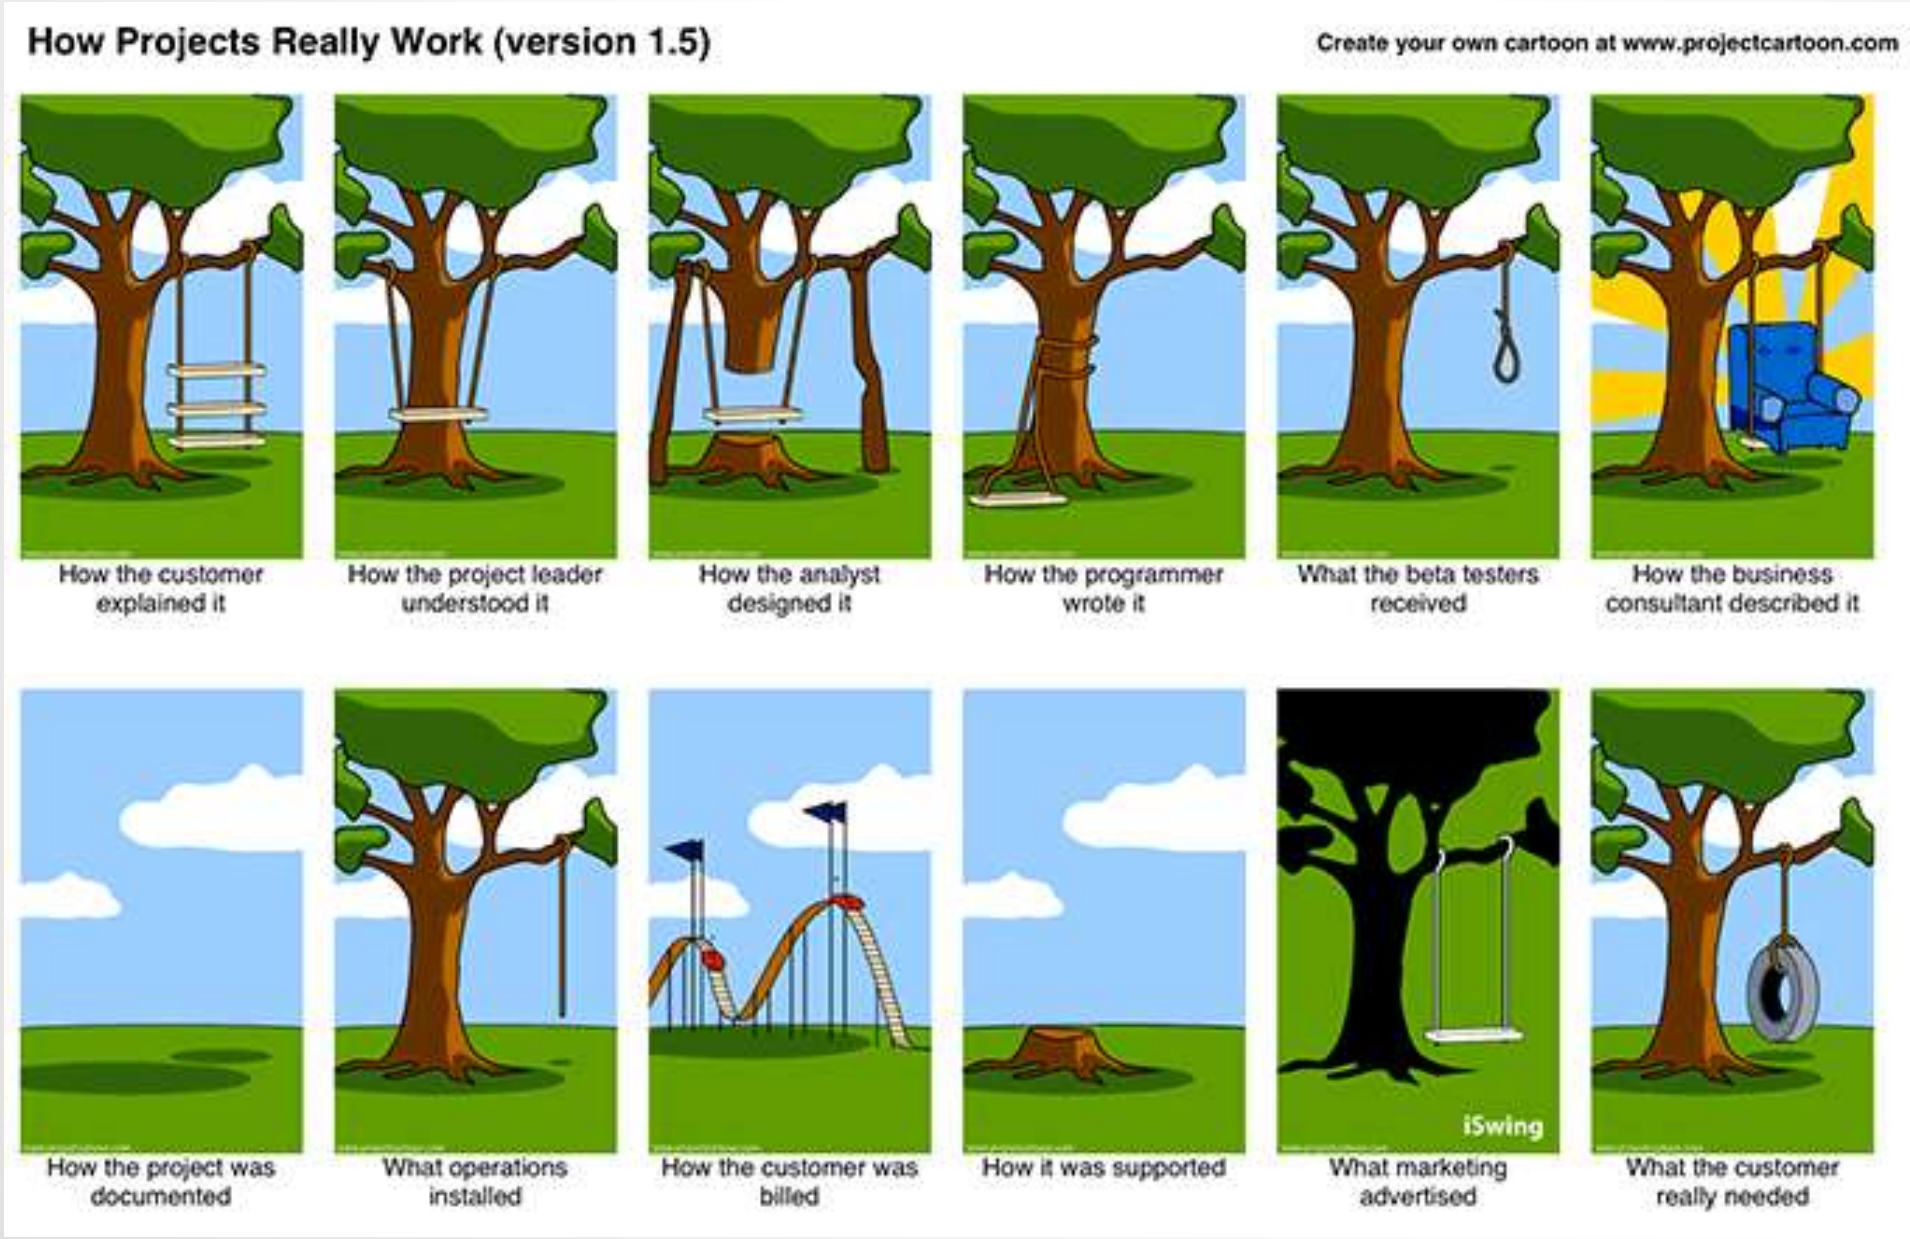

Source: Scrum Master – The 'Old' Waterfall Method (http://www.agile-scrum-master-training.com/agile-project-management/)

2 AGILE – What is?

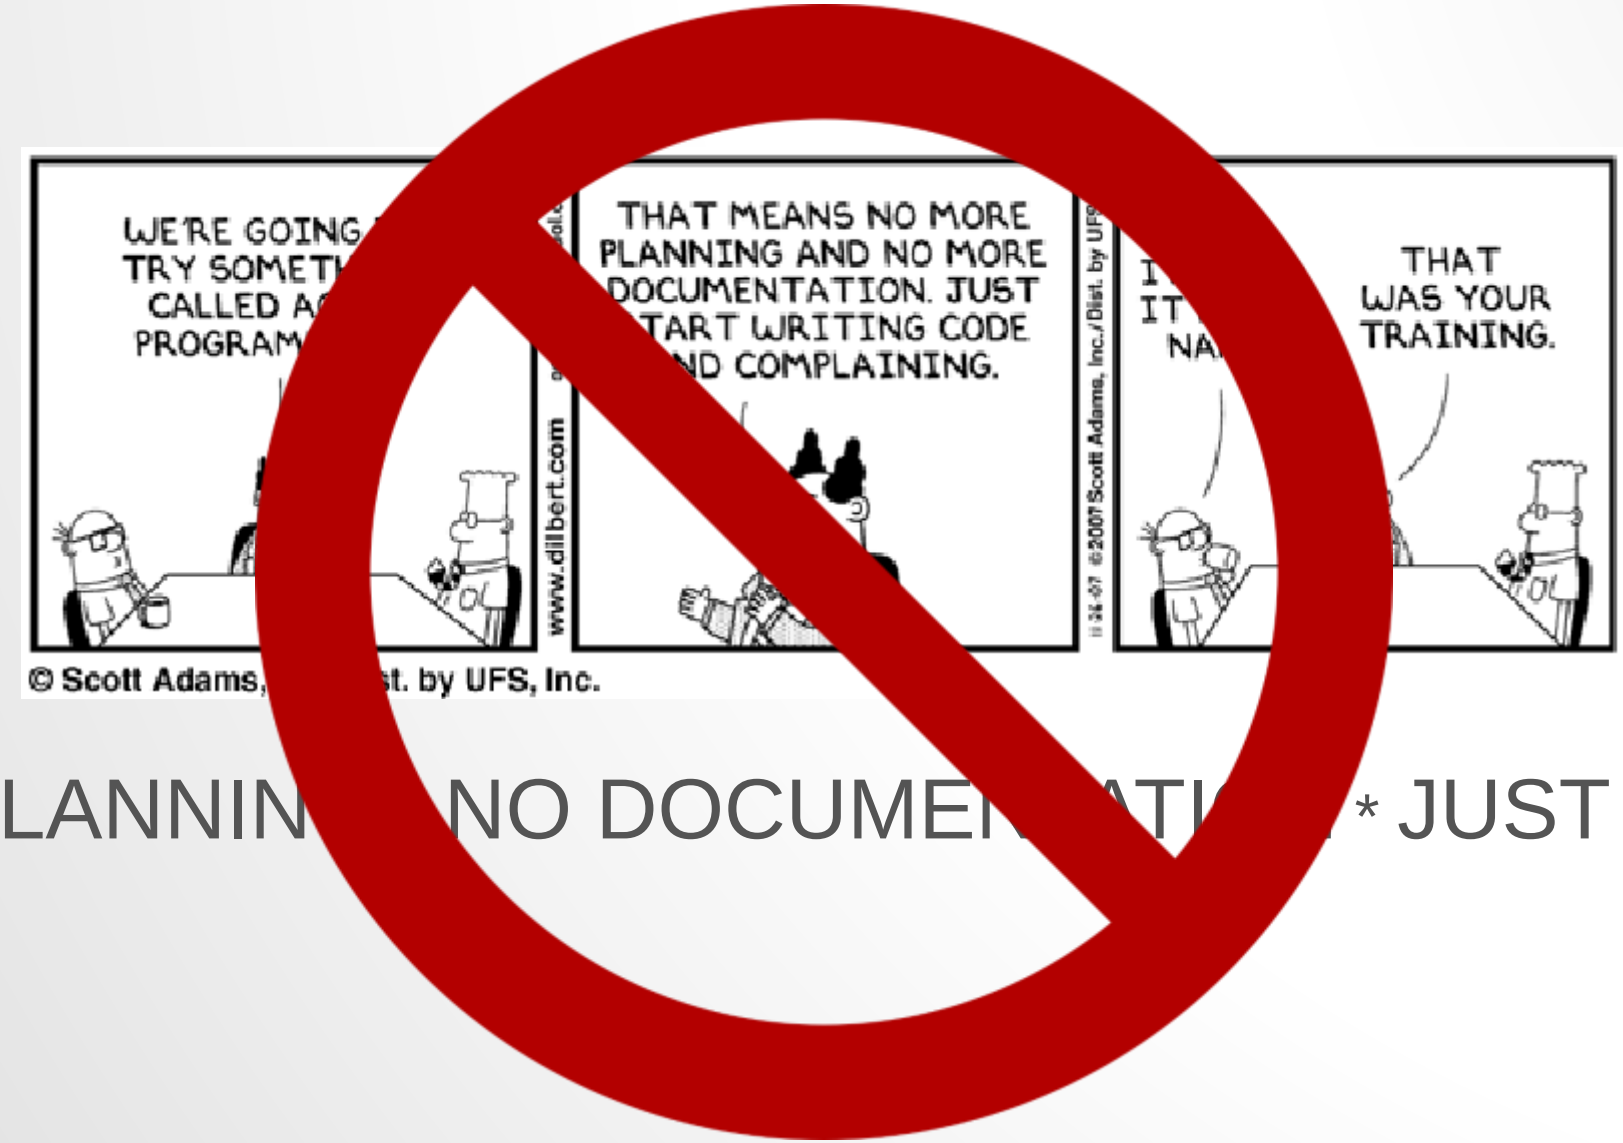

NO PLANNIN NO DOCUMEN ATI * JUST DO IT

2 AGILE – What is?



1. It is a **project management** with high **quality control** management.

2. Implies **leadership** philosophy but at the same time support **team work**, **self control**, **organization** and **accountability**.

3. A set of engineering **best practices** that allow for **rapid** delivery of high-quality product/project.

4. A **business framework** that align development with business/customer/company envision.


Images courtesy Dilbert(R) by Scott Adams

2 AGILE – What is?

Agile versus Traditional Project Management


Metrics	Traditional	Agile
Planning Scale	Long-term (> 6 months)	Short (3 – 6 months)
Interaction between customer and project team	Rare	Frequent
Time between specifications and implementation	Long	Short
Time to discover issues	Long	Short
Project schedule risk	High	Low
Ability to respond quickly to change	Low	High

3 AGILE Project Management Process Flow – The Standard Approach

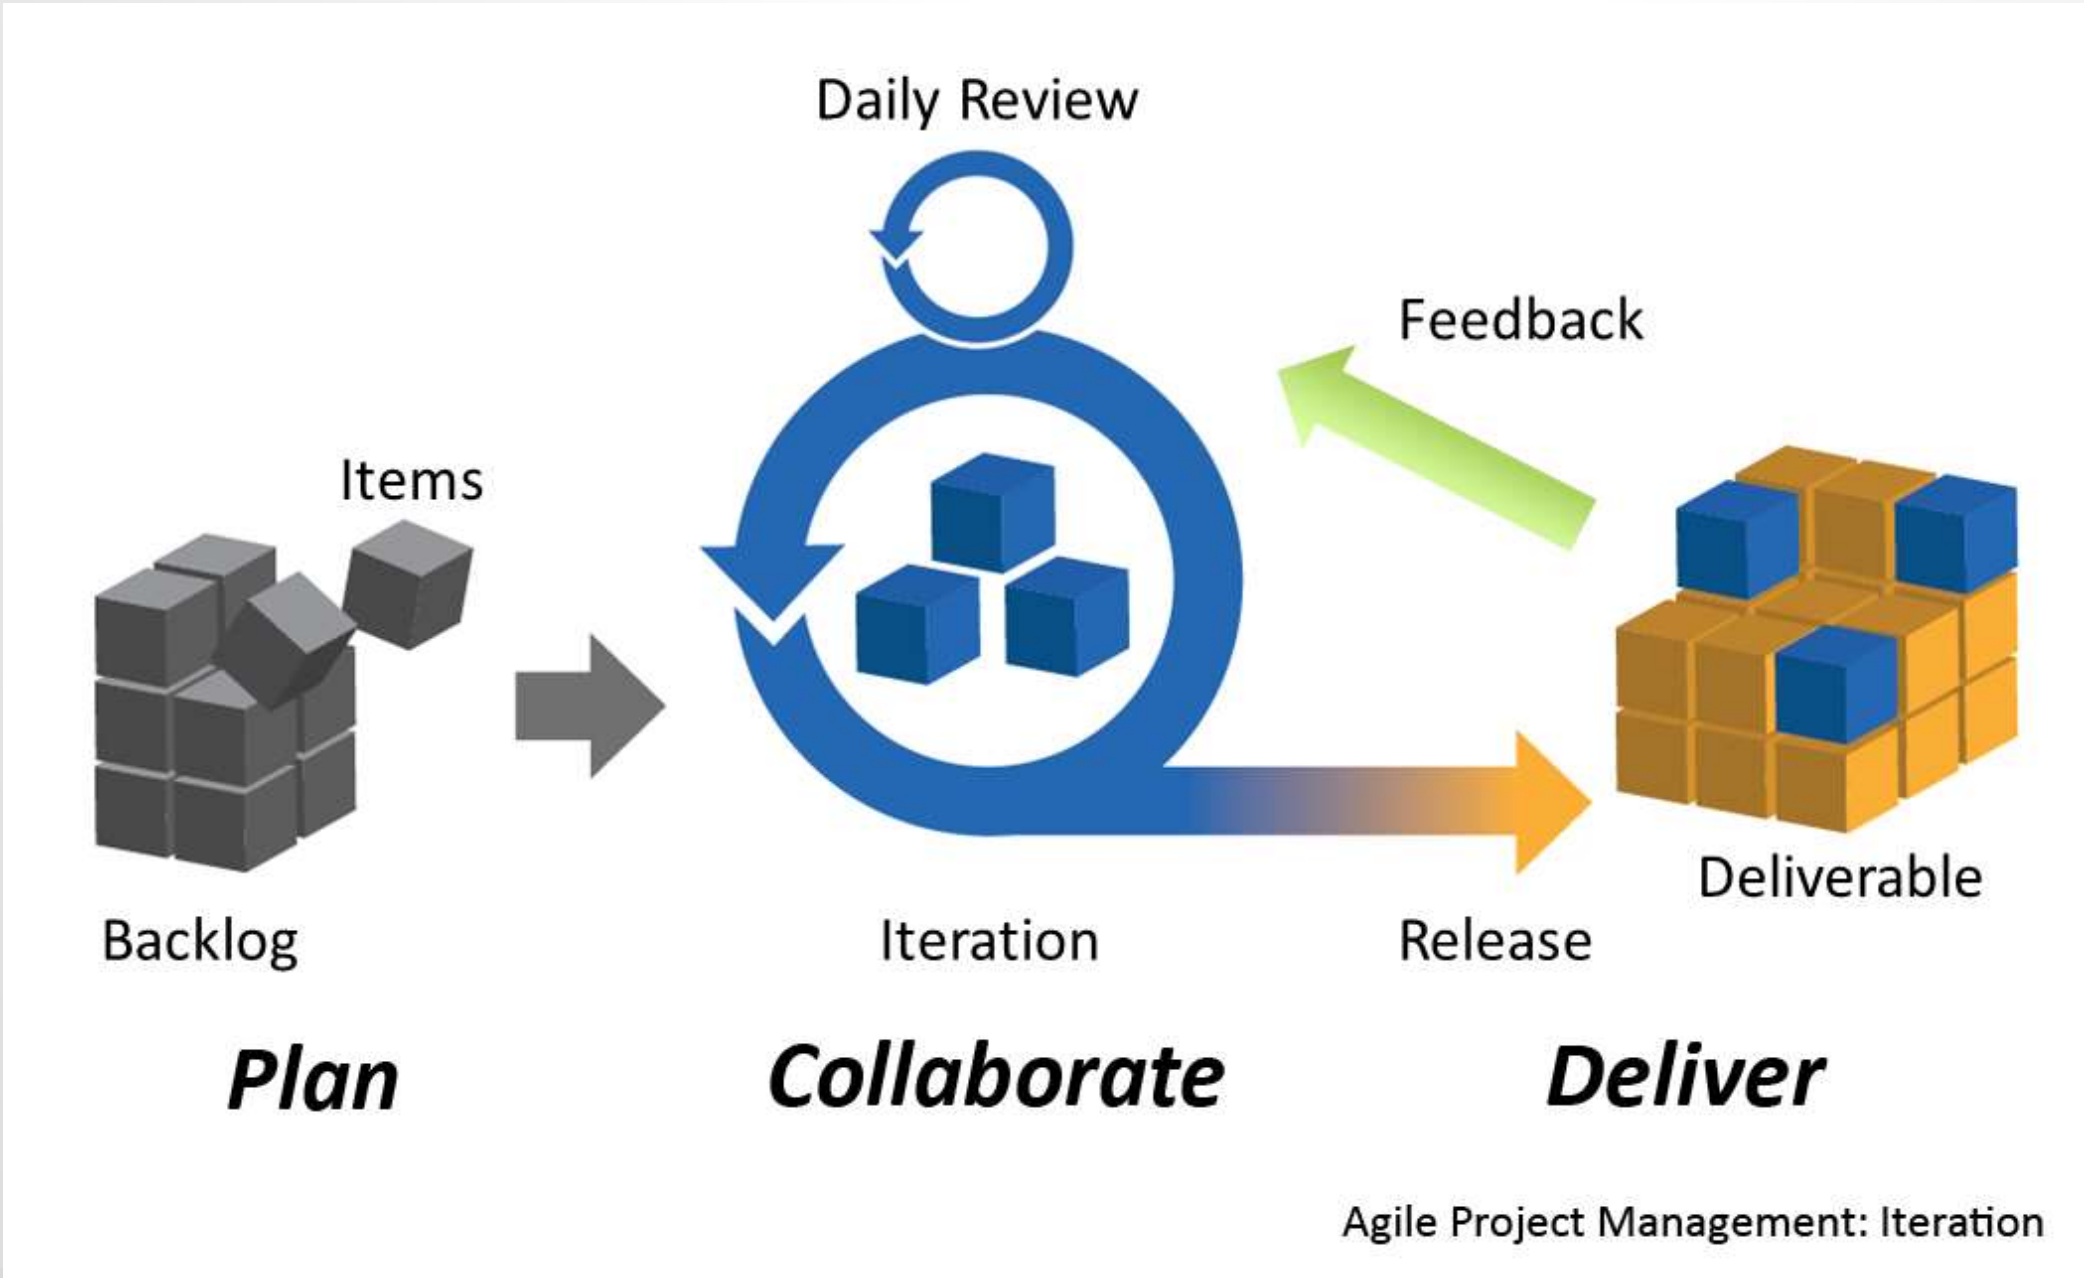


Source: Project Management Wikipedia (https://en.wikipedia.org/wiki/Project_management)

3 AGILE Project Management Process Flow – Adapting the process flow

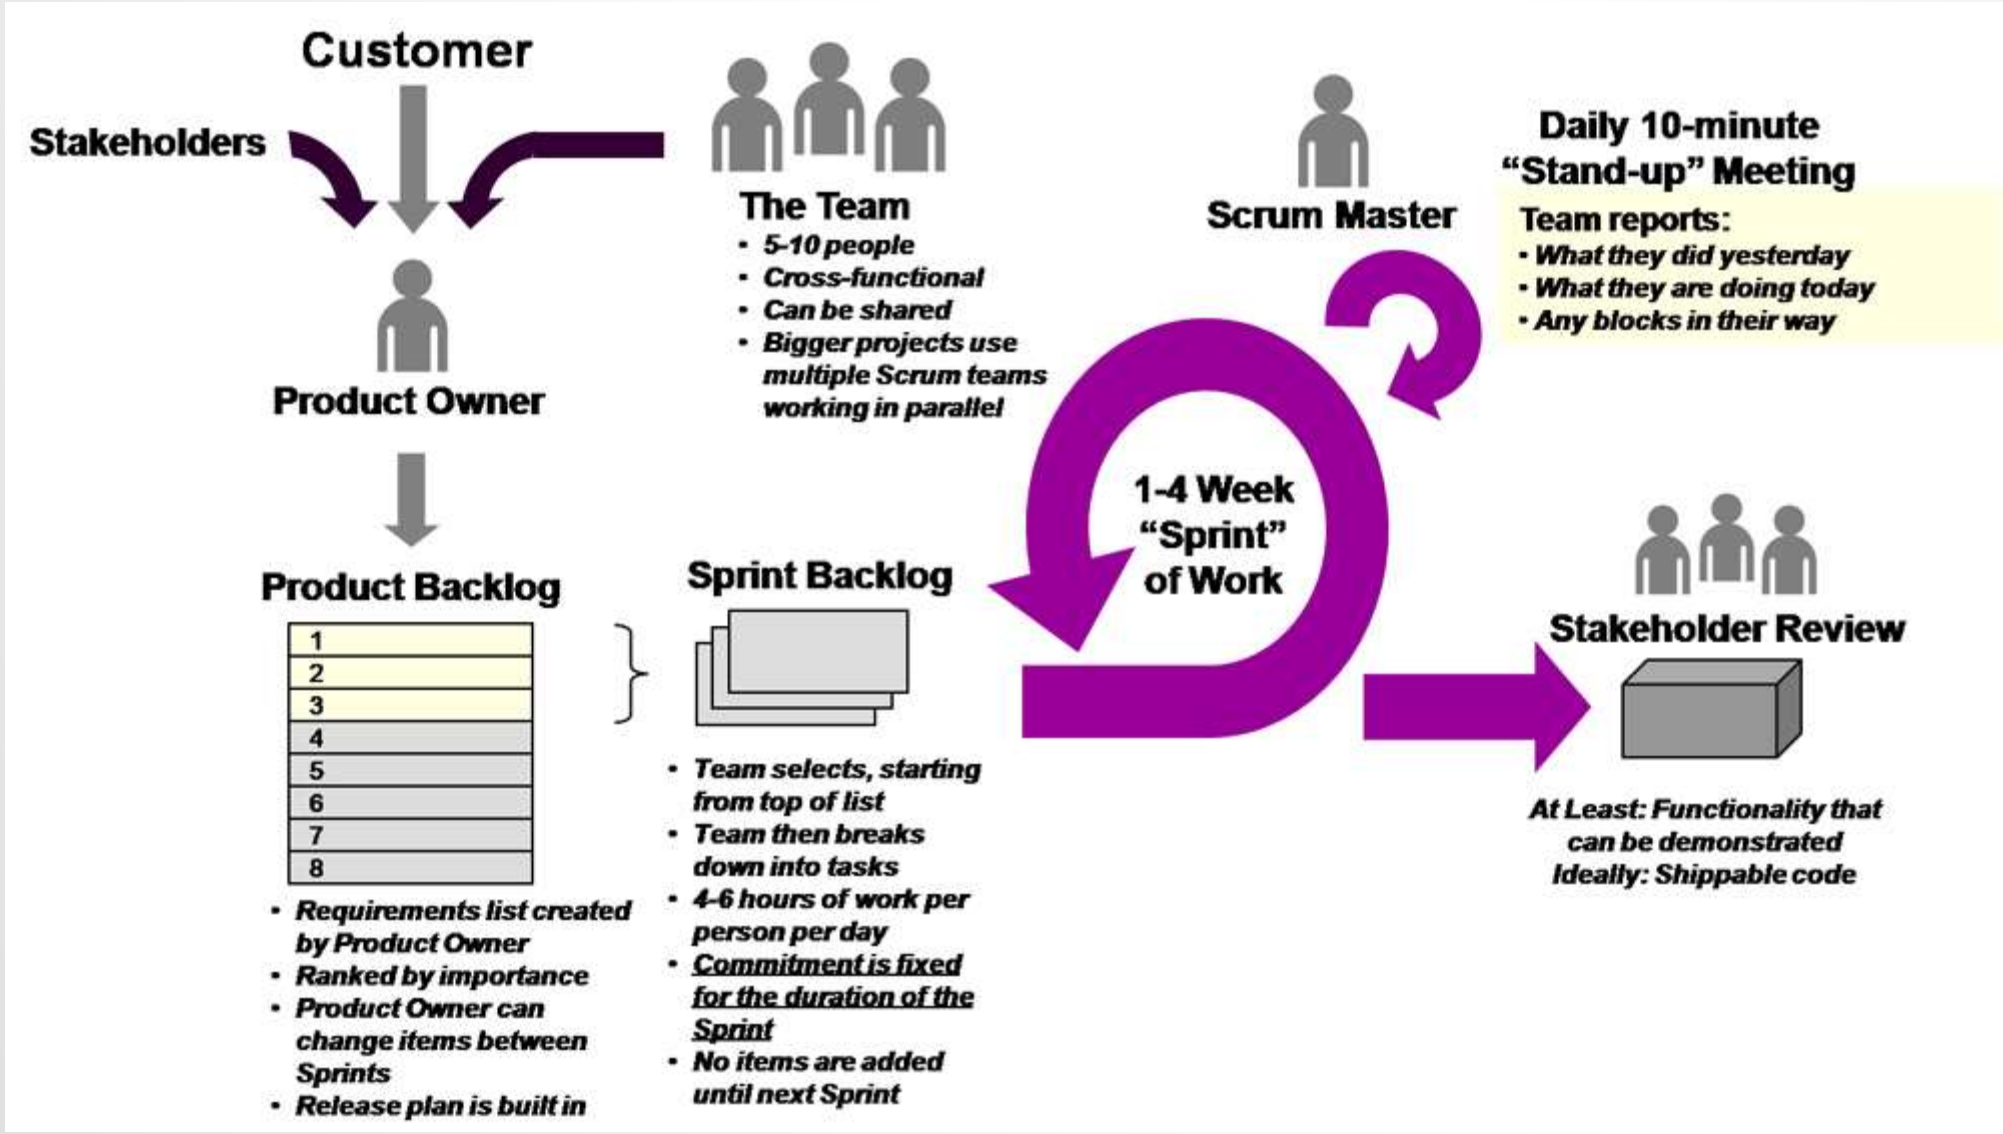


Source: Zen Ex Machina – The Blog (https://zenexmachina.wordpress.com/category/agile/page/2/)

3 AGILE Project Management Process Flow – Adapting the process flow

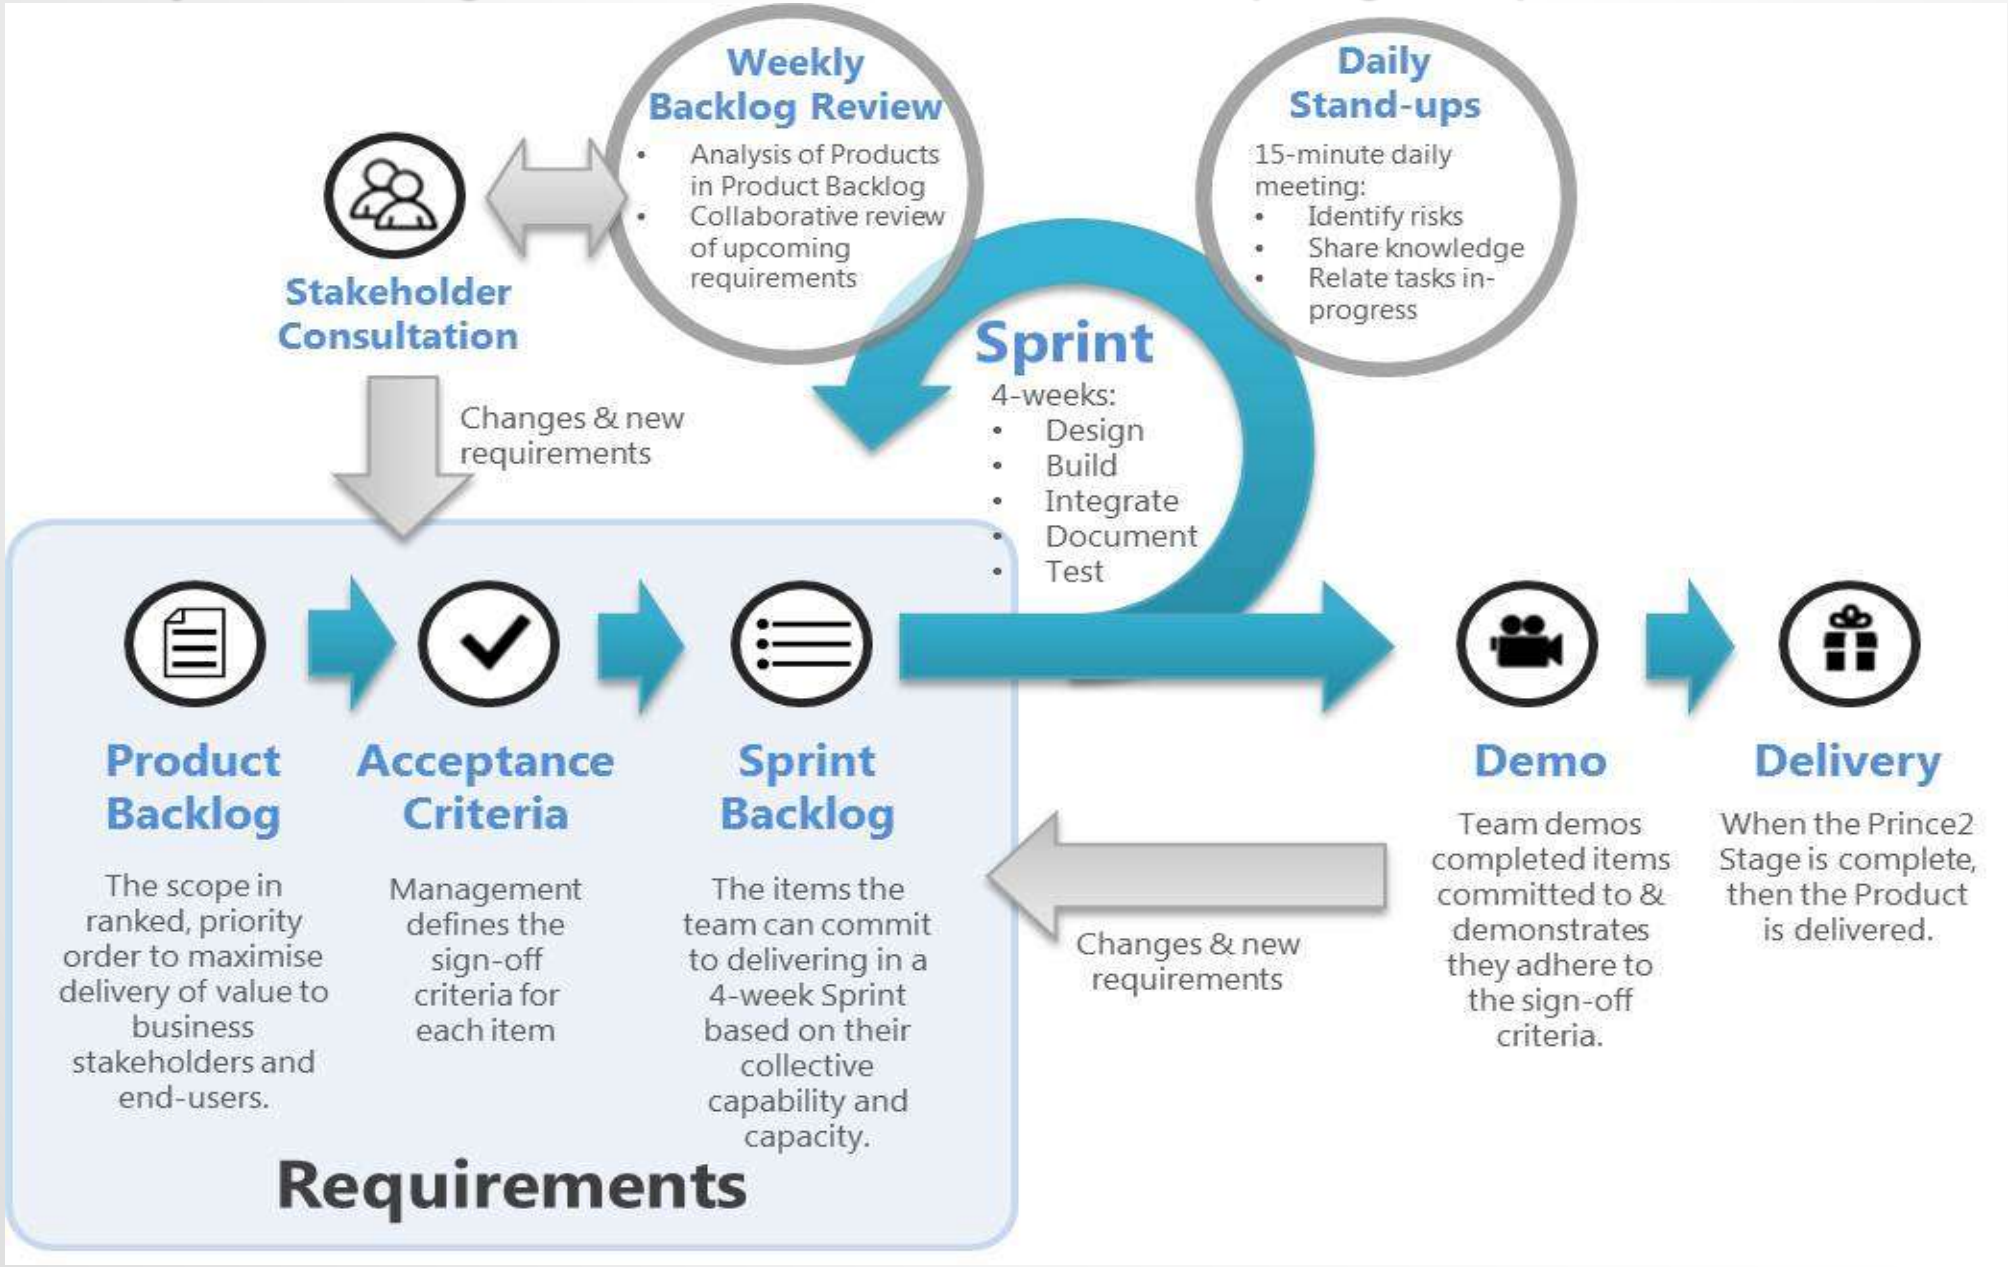


Source: Ian Mitchel - Scrum Alliance (https://www.scrumalliance.org/community/articles/2013/june/the-kanban-sandwich-a-bite-size-recipe-for-agile-w)


3 AGILE Project Management Process Flow – Adapting the process flow

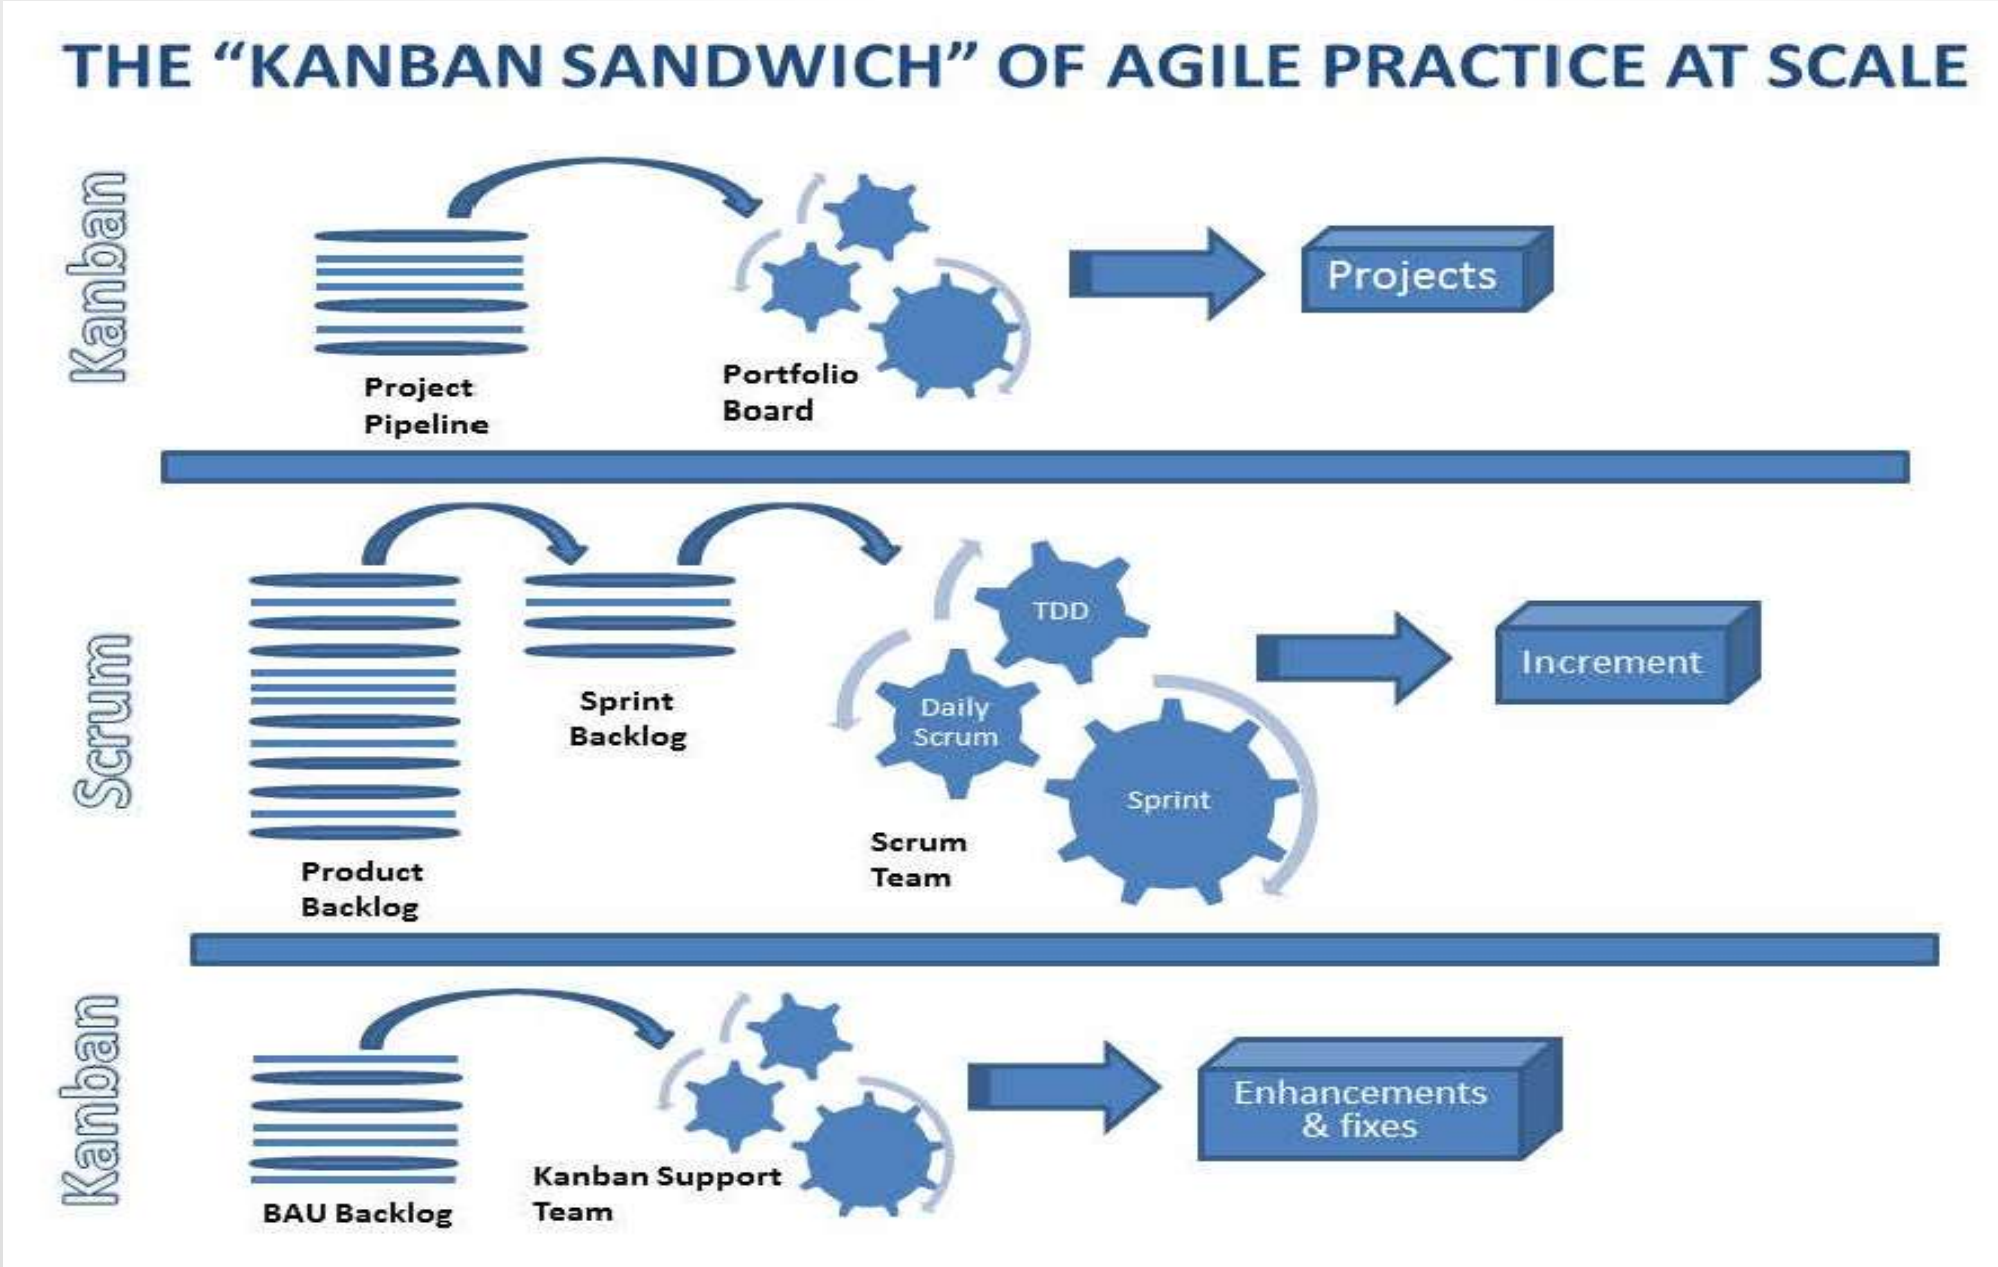

Source: Ian Mitchel - Scrum Alliance (https://www.scrumalliance.org/community/articles/2013/june/the-kanban-sandwich-a-bite-size-recipe-for-agile-w)

3 AGILE Project Management Process Flow – Adapting the process flow

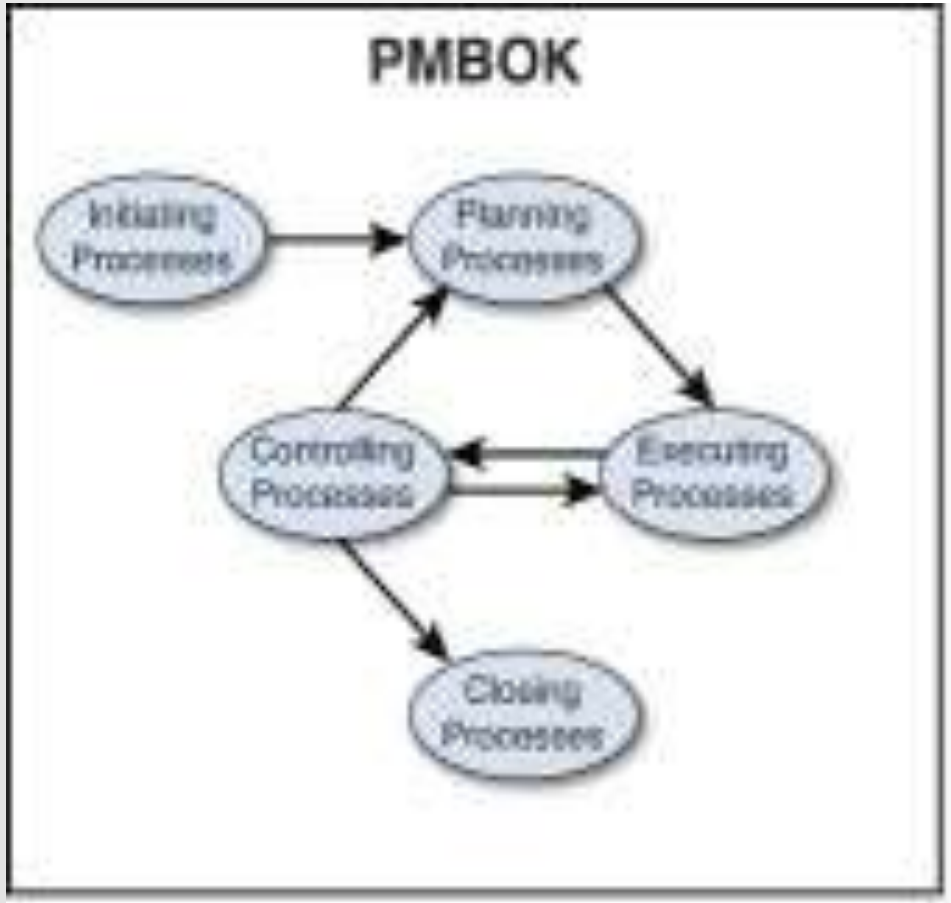


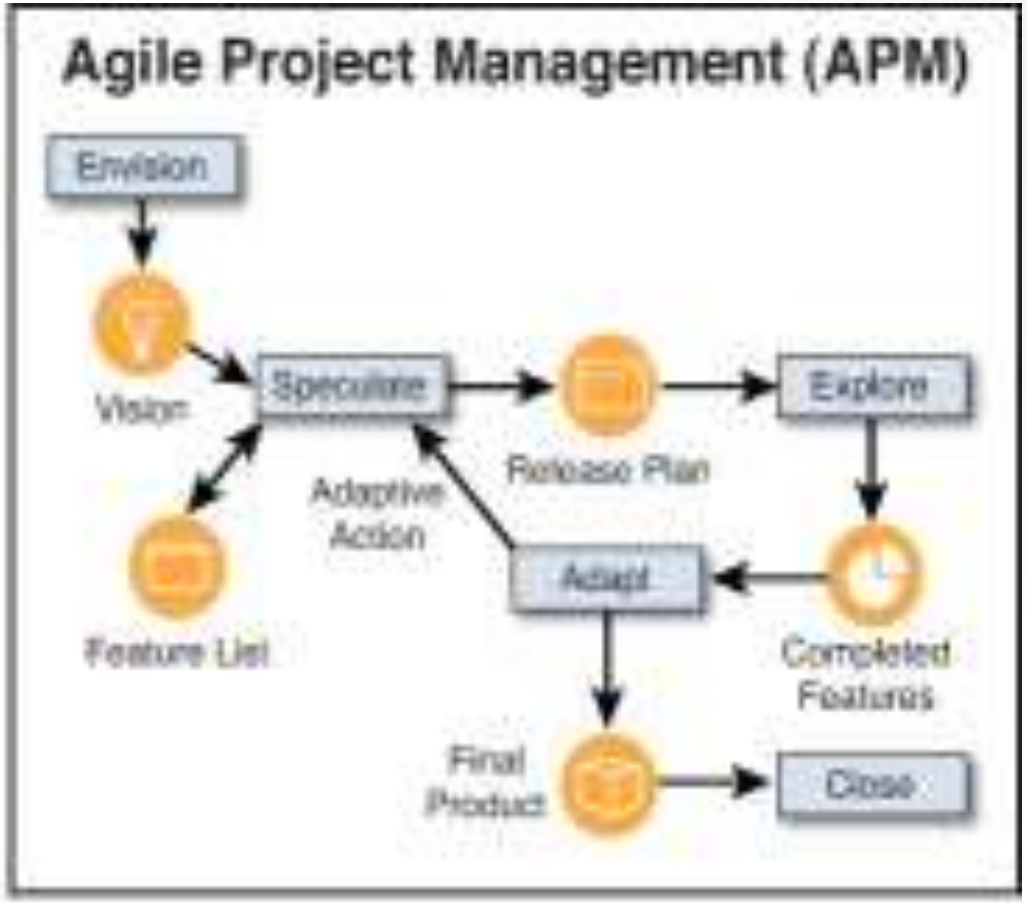

Initiating	Envisioning
Planning	Speculating
Executing	Exploring
Controlling	Adapting
Closing	Closing

Source: Gary Lister – Project Management Roots and Understanding the PMBOK Guide (FT Press – Pearson) (http://www.ftpress.com/articles/article.aspx?p=2261742&seqNum=12)

3 AGILE Project Management Process Flow – Actor and role

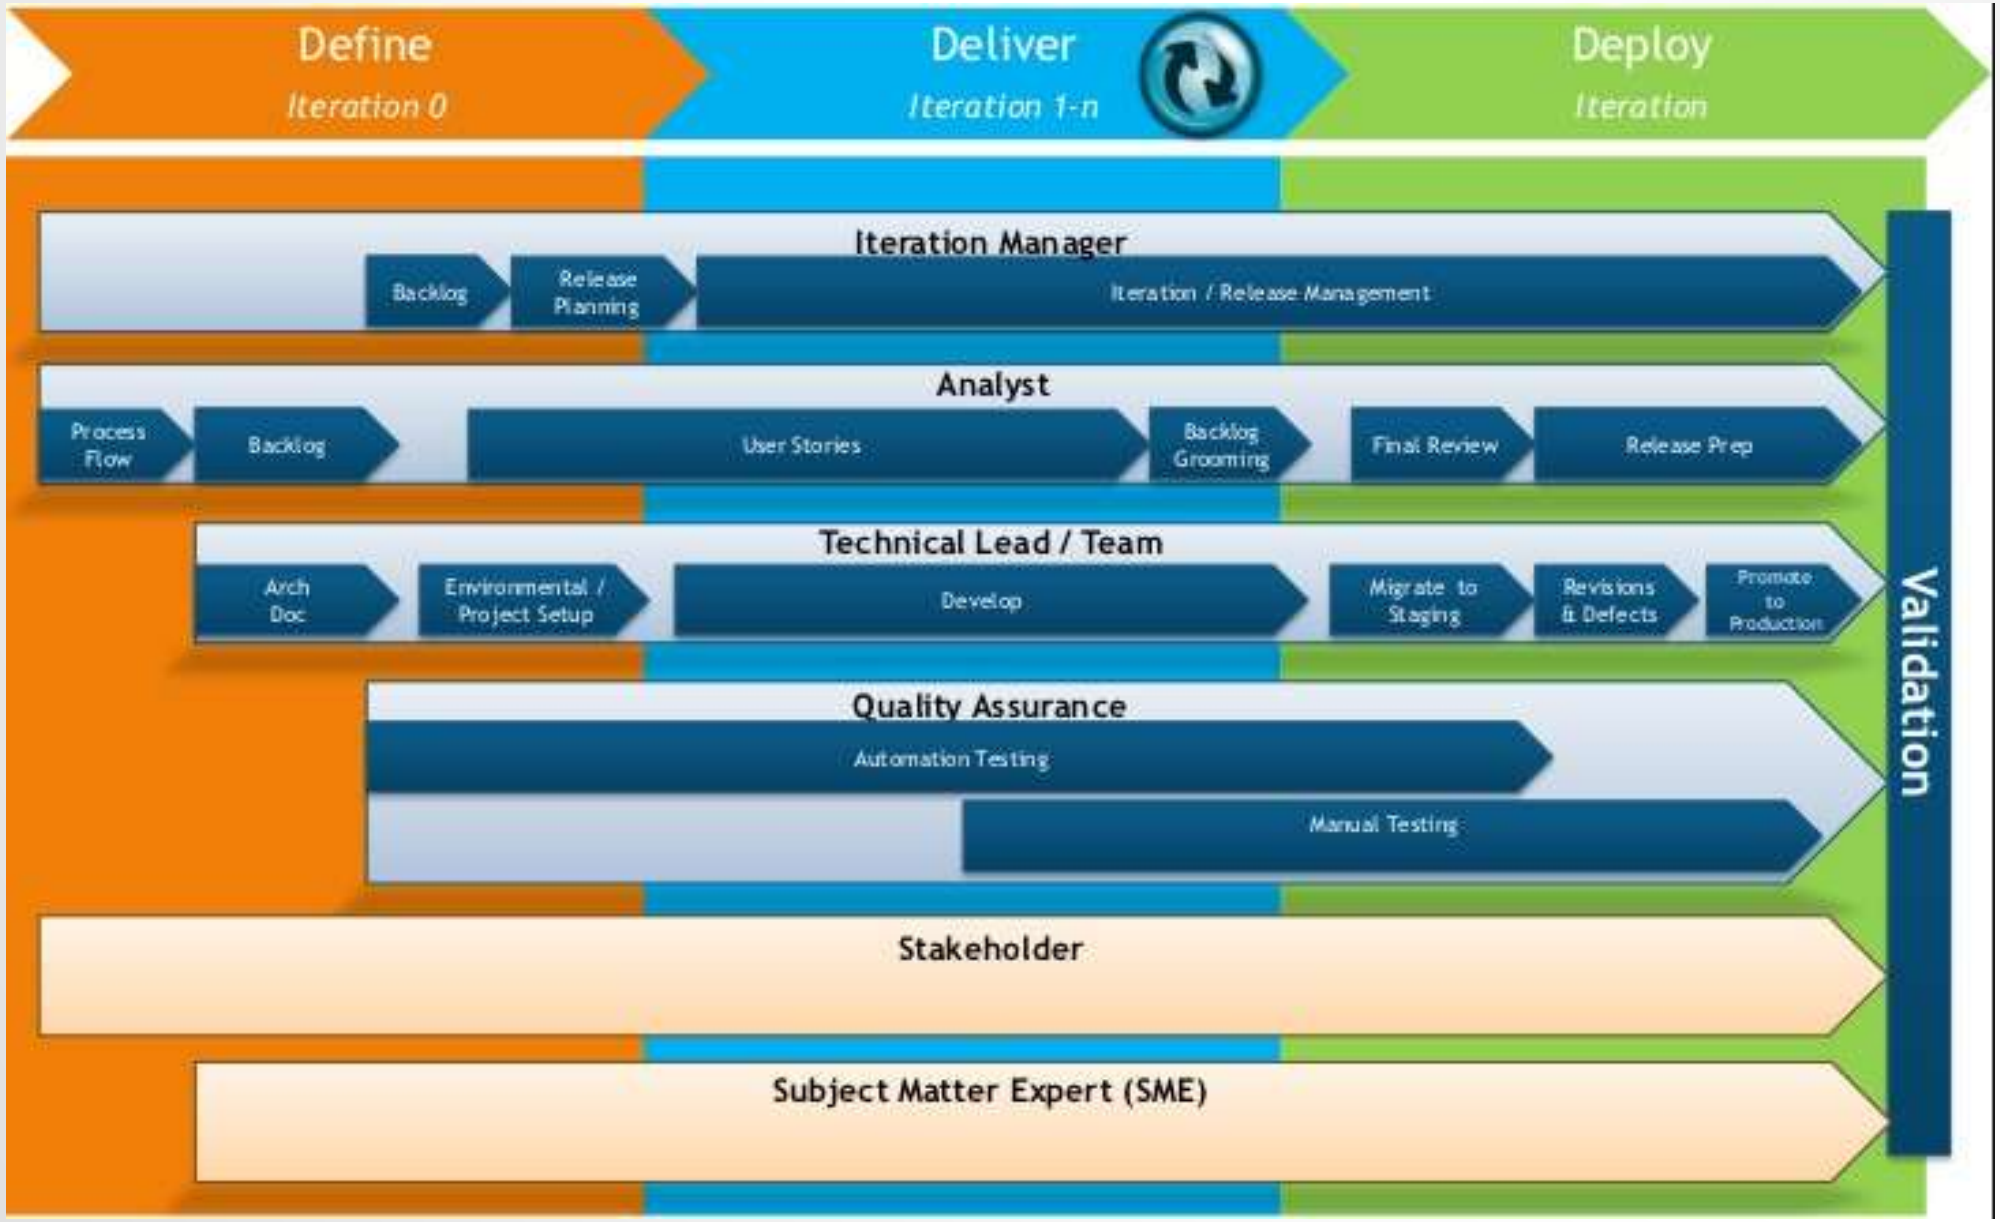

* This is basic role as recommended by Agile practitioner


4 Transition from Traditional to Agile



* PLANNING *

Source: Chuck Cobb (Udemy) – Mastering Agile Project Management for Project Managers (https://www.udemy.com/agile-project-management-overview-for-project-managers/)

4 Transition from Traditional to Agile

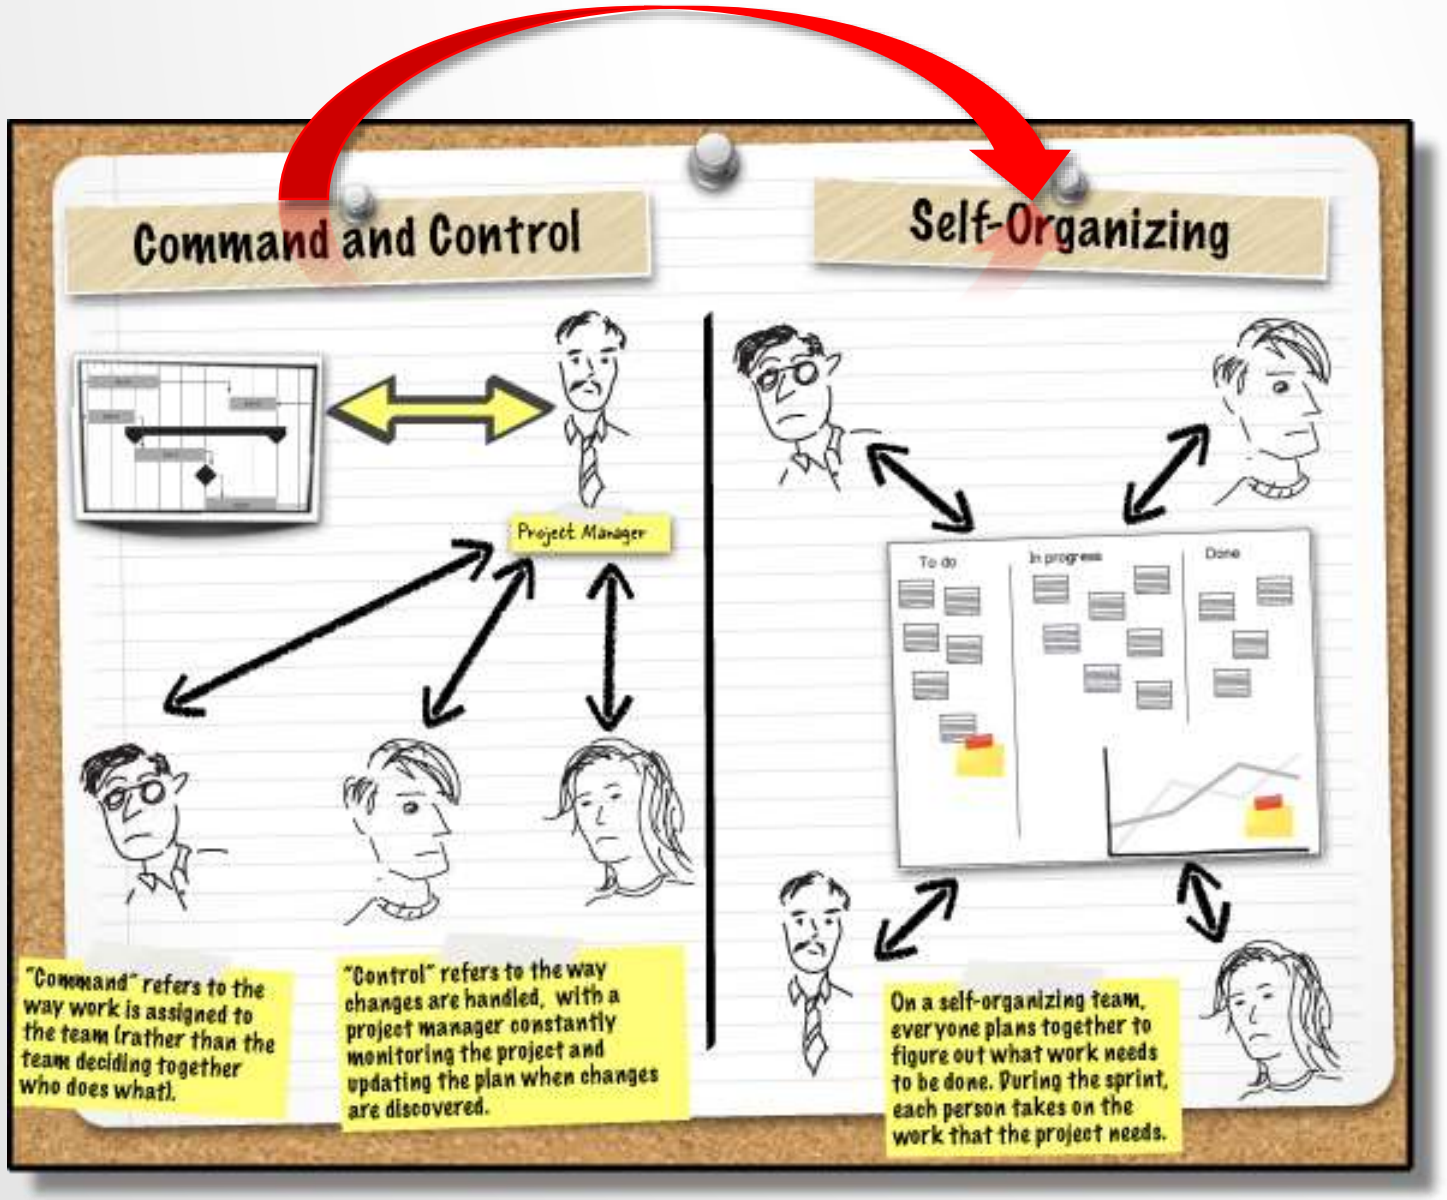

Source: Andrew Stellman (Building Better Software) – A Learning Agile Question from a business analyst (http://www.stellman-greene.com/2015/11/19/a-question-from-a-business-analyst/)

4 Transition from Traditional to Agile

Traditional Project Management	Agile Project Management
Focus on **plans and document artifacts**	Focus on **customer satisfaction** and interaction
Change controlled via **formal request process**	Change is expected, planned and **adapted as needed**
Resource-intensive **up-front planning**	Progressive, iterative, **rolling-wave planning**
Sponsor dictated, **scope-based delivery**	Product Owner prioritized, **time-boxed delivery**
Activity management via **work breakdown structure**	Task planning and execution flow based on **Team Member commitment**
Top-down **control**	Collaboration of **self-disciplined and self-organizing teams**
Rigid, **formal** management methods	Minimal set of **loose guidelines and best practices**

4 Transition from Traditional to Agile



5 Steps to successfully apply agile

1. Get the complete story
2. Empower your team member
3. Prioritize the deliverables
4. Estimate the load and resources carefully
5. Always update/do check-point

S.M.A.R.T.

Image from: Shanaka Nagasinghe via LinkedIn (https://www.linkedin.com/pulse/impact-agile-project-management-practices-enhancing-nagasinghe-pmp-)

5 Applying Agile

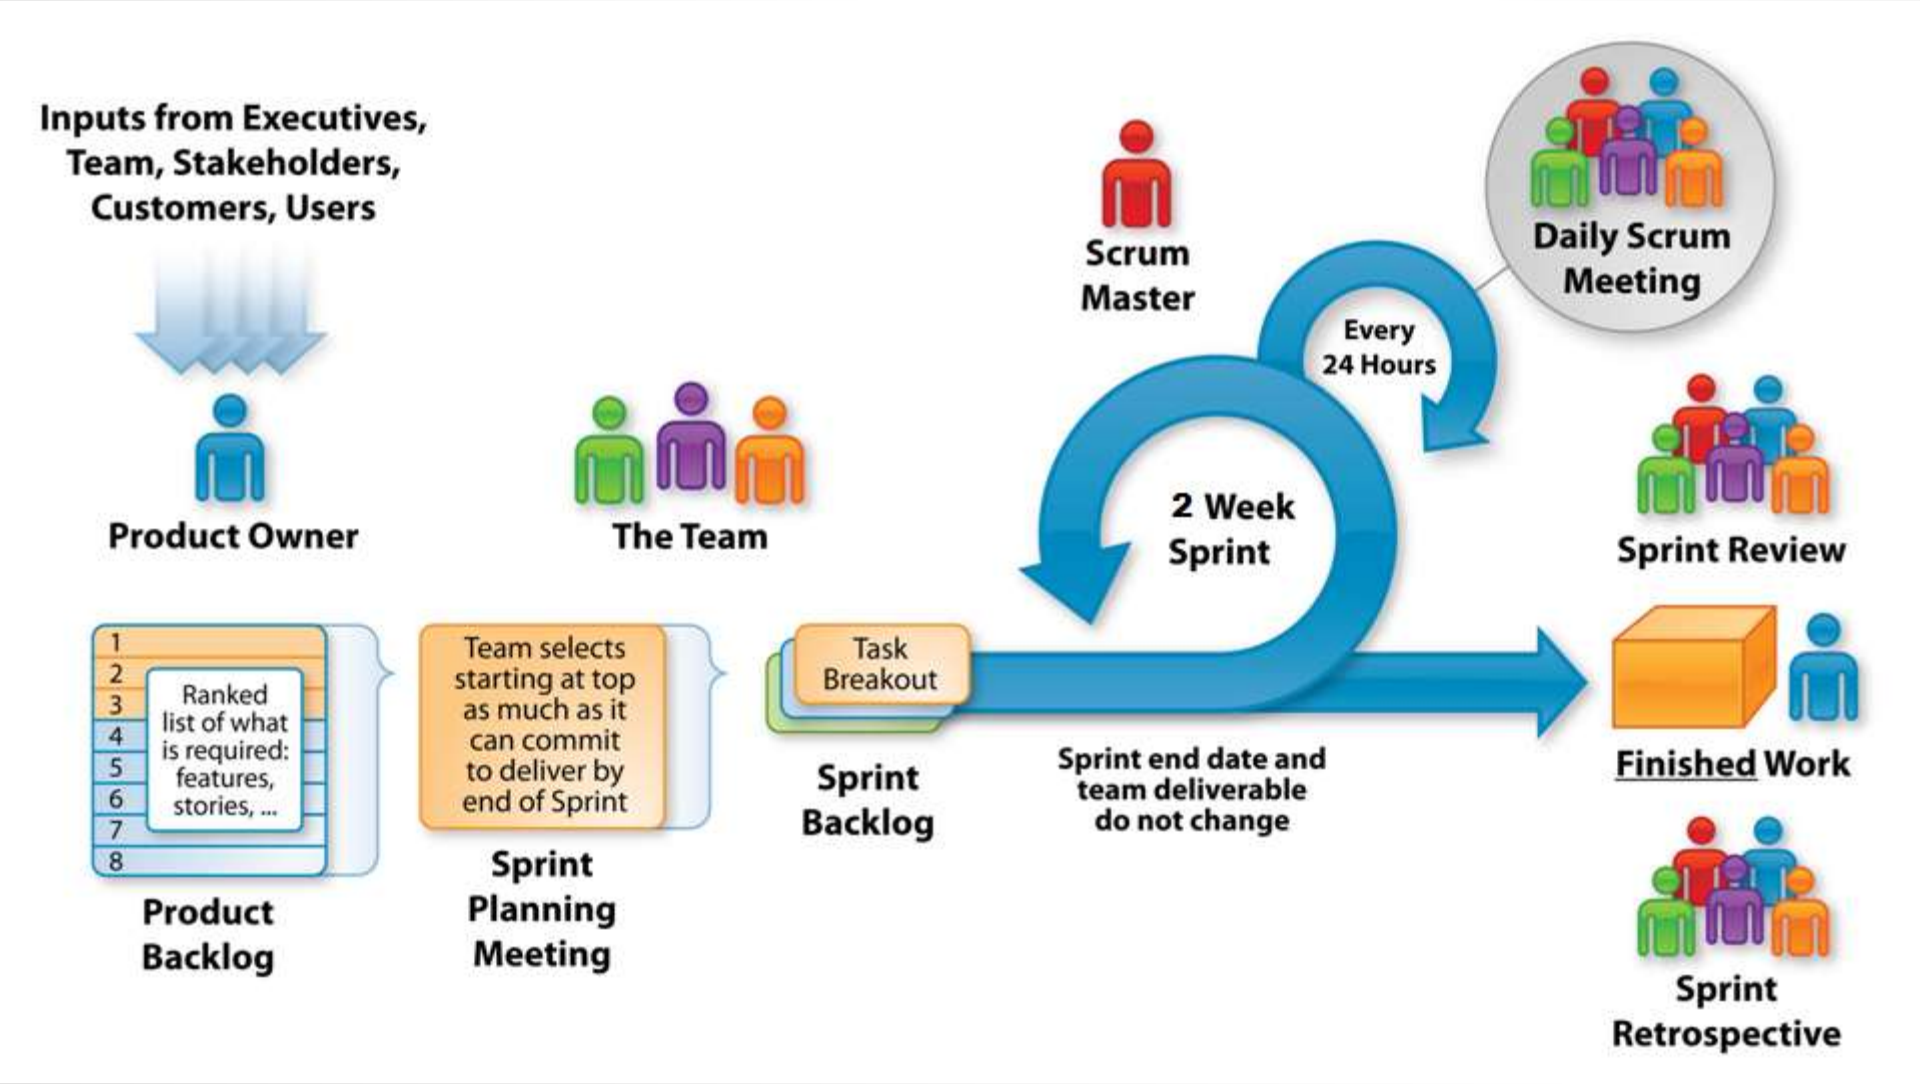


Image from: Ravi Kumar – What is the Scrum Process Flow (http://www.etechpulse.com/2015/02/agile-scrum-process-sdlc.html)

5 Applying Agile

The simplest Agile consist of:

1. **General Information** – Stakeholder, Project Owner, Team members, Objective and Measurement of the project.
2. **Meeting / Discussion notes** – Date/time, Subject, Discussion and Action item.
3. **Decisions** – Product Owner / Stakeholder decisions based on sprint demo
4. **Commitment** – Based on decision/sprint result, what is the commitment and PIC of each agreed commitment.
5. **Risk** – The risk capture during the Sprint/Scrum process, severity and mitigation plan.
6. **Project Timeline** – In a WBS mode divided in the following context
    1. Story/Deliverables/Functions/Features - Iteration
    2. Scrum List – List of deliverables for the identified iteration
    3. Sprint backlog/list – List of activities to do for each deliverable

1. Each of the Sprint will have:
    1. Timeline / Sprint
    2. PIC
    3. Review
    4. Backlog – audit trail
    5. Status

5 Applying Agile – Sample General Info

Project Code:	ITD-CORP-2015-001
Project Name:	On Boarding System Phase 1
Business Users:	Corporate Human Capital Division (HCD)
Project Lead:	-
Technical Lead:	-
Team Members:	ITD - Mohd Nizar Abd Azik (MNA), Nurul Haszeli Ahmad (NHA), Suhaimi Maidin (SM) HCD - Suzani Taslim (ST)
Start Date:	-
Duration:	6 Months
Project Description:	On boarding system is an initiative by HCD with the help from ITD to digitize current manual process for new employee upon acceptance of offer and before on board as Prasarana employee.
Project Goal:	To digitize current process for onboarding process.
Measurement:	Successful implementation and adoption by HCD
	Successfully improve process flow and processing time
	Reduce cost of printing (subjective)

5 Applying Agile – Sample Meeting Notes

Product Owner Meeting Notes			
Date	Subject	Discusion	Action
14-Aug-2015	Iteration 1 demonstration	HCD request to access it for pre-demonstration with HOD	MNA to release the system at staging/test server for HCD trial
		Change of form listing and sequence	MNA to update the system with changes
		Iteration 2 is expected to complete and demonstrated to HCD and GD of HCD by middle of September	MNA to set reasonable date with ST by middle of September
08-Sep-2015	Iteration 1 Sprint 2 demonstrated	Pn Ruswati request few changes on the field and the content	MNA to update the system with changes
		Pn Rohana will share latest STD	NHA to follow up with Pn Rohana
		Releasing Phase 1 for used	MNA will release the system (Phase 1) for used by October 15th.
30-Sep-2015	CMC Presentation	MHA - update the slide with additional info	NHA - to update the slide on architecture, process flow and RACI
		Pn Ruswati - To share the info with CHRO after 7-Oct-2015	NHA - to check with Pn Suzani / Pn Rohana on CHRO availability after 7-Oct-2015

5 Applying Agile – Sample Decision Log

Product Owner Decisions			
#	Raised	Action	Owner
1	14-Aug-2015	Change of form listing	MNA
2	14-Aug-2015	Dashboard showcase to GD HCD before mid september	MNA/ST
3	08-Sep-2015	To present to GD by October	MNA/ST
4	08-Sep-2015	To release to production by October 15	MNA/NHA/SM
5	30-Sep-2015	To present to CHRO after 7-Oct-2015	MNA/NHA/SM
6			
7			
8			
9			

5 Applying Agile – Sample Commitment Log

Product Owner Commitments						
#	Raised	Action	Owner	Ready by	Complete	Remark
1	14/08/2015	Iteration 1 Demonstration	MNA, NHA, ST		Done	
2	14/08/2015	Release to Staging/Test Environment	MNA		Done	Released on 28/08/2015. Delay 1 week
3	28/08/2015	Iteration 1 - Bug Fix and Update changes based on comment during demo	MNA		Done	Completed on time.
4	28/08/2015	Iteration 1 - Demonstration to HCD HOS	MNA, NHA, ST		Done	Demo to Pn Ruswati and Pn Rohana on 08/09/2015
5	08/09/2015	Iteration 1 - Demonstration to HCD GD	MNA, NHA, ST		WIP	Plan to execute on 03/10/2015 To check with Pn Suzani on 7-Oct-2015 as CHRO not available until the date (Hajj)
6	08/09/2015	Release Server to production	MNA		WIP	Plan to complete by 15-Oct-2015 30-Sep-2015: Presented In CMC - Plan to release on 13-Oct-2015
7						
8						


5 Applying Agile – Sample Risk Log

Risk Log							
#	Raised	Description	Impact	Severity	Action	Owner	Complete
1	04-Sep-2015	Production Environment not ready	Delay of go-live date	Low	Work with Infra Team	MNA, NHA	WIP
2	21-Sep-2015	SSL not ready	Delay of go-live date for external	Low	Work with Infra Team	MNA, NHA	WIP
3							

5 Applying Agile – Sample Project Timeline

	A	B	C	D	E	F	G	H	I	J	K	L	M	N
1				Tentative Date		Actual Date		Plan Duration (days)	Actual Duration (days)	% Complete	Status			Remar
2	WBS	Task Descriptions	Responsible	Start	End	Start	End					09-Sep-2015	18-Sep-2015	21-Sep-2015
3	1	Iteration 1	MNA, NHA, SM, ST	01-Jun-2015	15-Nov-2015	01-Jun-2015	15-Nov-2015	121	121	63%	WIP			
4	1.1	Development	MNA, SM	01-Jun-2015	15-Nov-2015	01-Jun-2015	15-Nov-2015	121	121	89%	WIP			
17	1.1.6	Testing	MNA, NHA, SM, ST, IT	21-Jun-2015	30-Sep-2015	21-Jun-2015	30-Sep-2015	74	74	60%	WIP	07/09/2015 - MHA request to open to Junior Shaper for testing	Application is updated based on comment by HCD. Will released to production for testing by first week of	
18	1.1.7	Review	MNA, NHA, SM, ST	19-Jun-2015	15-Nov-2015	19-Jun-2015	15-Nov-2015	107	107	70%	WIP	08/09/2015 - 2nd Review done with HCD (Pn Rohana & Pn Roswati). There will be final review before going to live with HCD	Plan to present between 7th to 9th October (subjected to HCD availability)	
19	1.1.8	Bug Fixing	MNA	19-Jun-2015	15-Nov-2015	19-Jun-2015	15-Nov-2015	107	107	80%	WIP	09/09/2015 - Bug Fix and update based on review on 08/09/2015.		
20	1.2	Deployment	MNA, NHA, SM, Infra	21-Jun-2015	15-Oct-2015	21-Jun-2015	15-Oct-2015	85	85	100%	Done			
24	1.2.2	Production Server Readiness	MNA, NHA, SM, Infra	28-Aug-2015	15-Oct-2015	28-Aug-2015	03-Nov-2015	36	49	100%	Done	CMC Preparation - Plan to go for CMC on 29/09/2015	SSL Certificate in progress - Updated by Infra on 18/09/2015	Norliza - PO release last week. S be ready within this week.
25	1.2.2.1	Configure Server	Infra	28-Aug-2015	15-Oct-2015	28-Aug-2015	26-Oct-2015	36	43	100%	Done	Server @ Subang Release for Applications setup	(MNA) - DB and Application setup is still in progress	
26	1.2.2.2	Release Server	MNA, NHA, SM	28-Aug-2015	15-Oct-2015	28-Aug-2015	15-Oct-2015	36	36	100%	Done			
27	1.3	Documentation	MNA, NHA	03-Oct-2015	15-Oct-2015	03-Oct-2015	15-Oct-2015	10	10	65%	WIP			
31	1.3.2	User Manual	MNA, NHA	03-Oct-2015	15-Oct-2015	03-Oct-2015	15-Oct-2015	10	10	30%	WIP			
32	1.3.2.1	Create document	NHA	03-Oct-2015	15-Oct-2015	03-Oct-2015	15-Oct-2015	10	10	50%	WIP			
33	1.3.1.2	Release document	NHA	03-Oct-2015	15-Oct-2015	03-Oct-2015	15-Oct-2015	10	10	10%	WIP			
34	1.4	Training	MNA	16-Oct-2015	17-Oct-2015	16-Oct-2015	17-Oct-2015	2	2	0%	Not Started			

Q & A

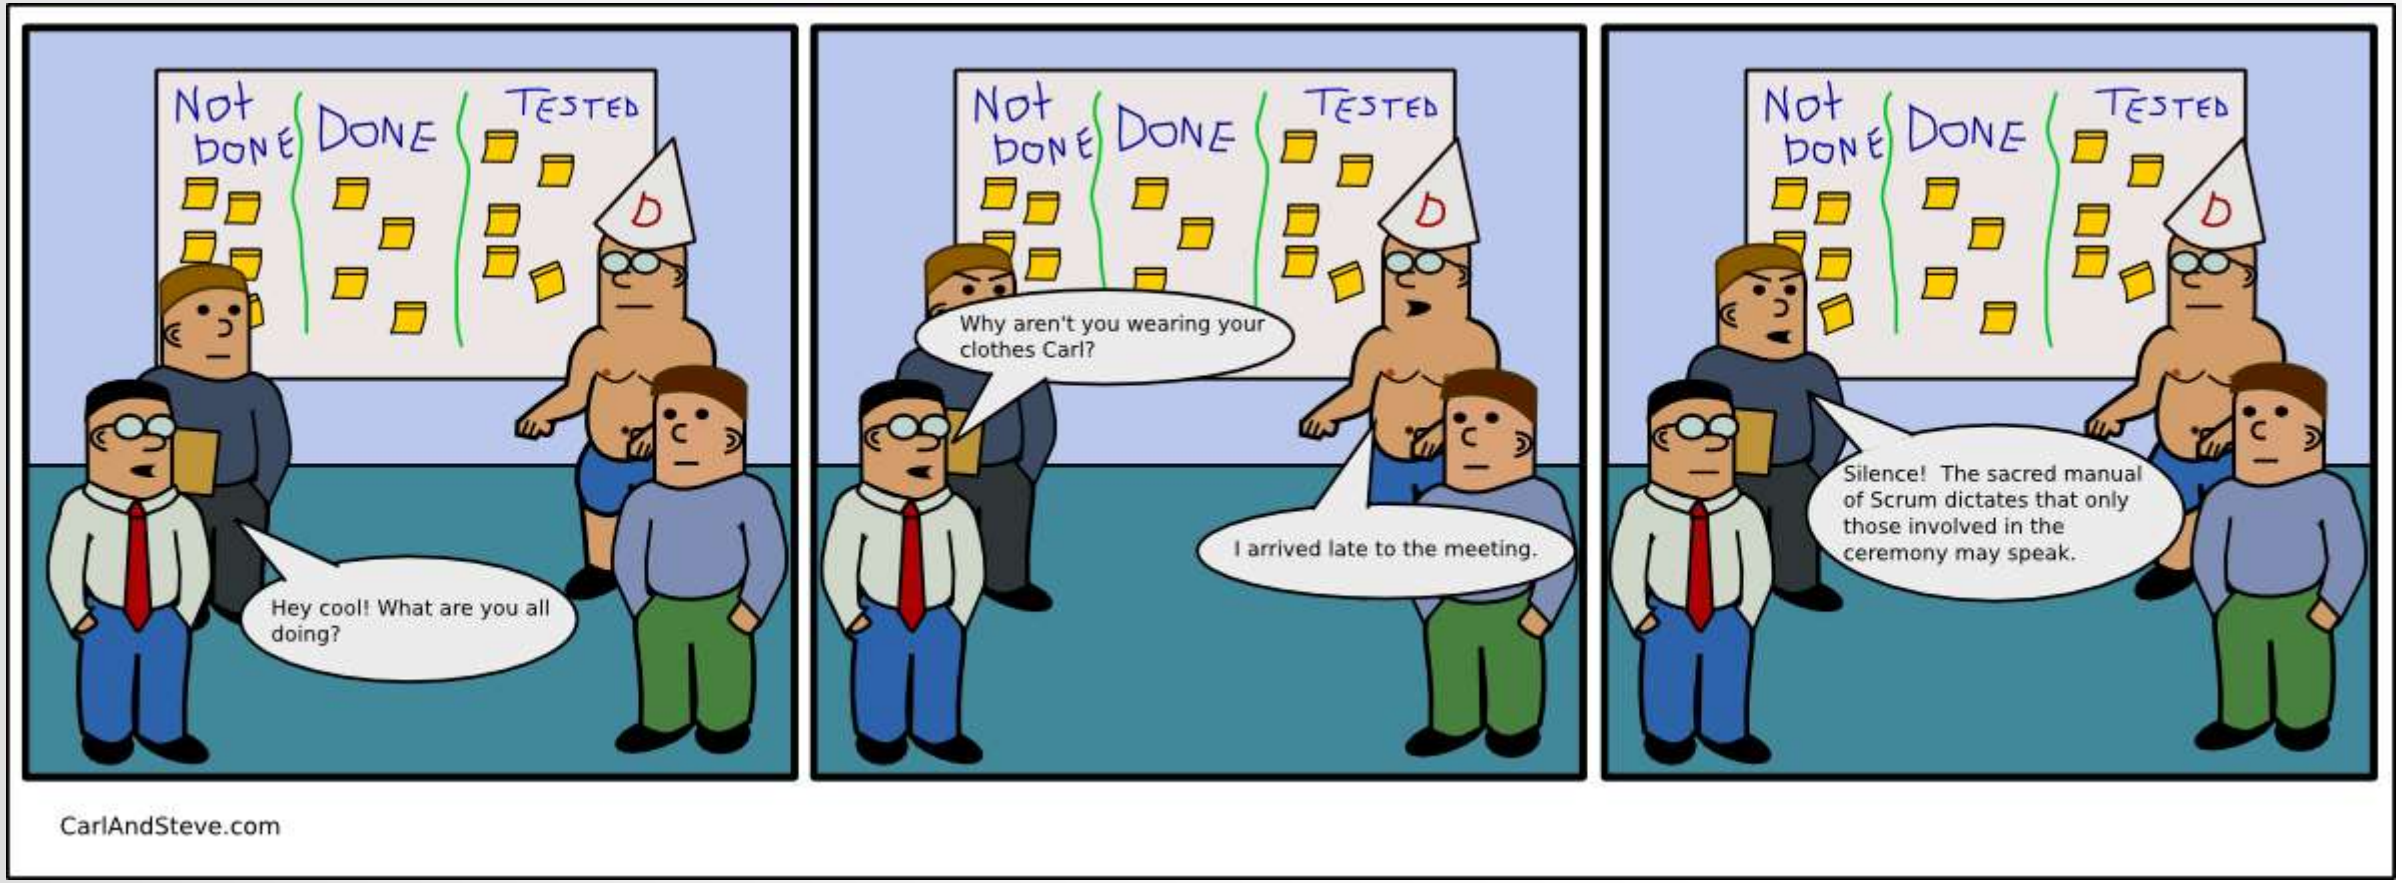
Not done
Done
Tested
Hey cool! What are you all doing?
Why aren't you wearing your clothes Carl?
I arrived late to the meeting.
Silence! The sacred manual of Scrum dictates that only those involved in the ceremony may speak.
CarlAndSteve.com

References:

1. PMBOK Guide 5th Edition – Project Management Process
2. Wikipedia – Project Management Wikipedia (https://en.wikipedia.org/wiki/Project_management)
3. Project Management Tips (http://pmtips.net/Blog/adapting-agile-methodology-startup)
4. Zen Ex Machina – The Blog (https://zenexmachina.wordpress.com/category/agile/page/2/)
5. Ian Mitchell - Scrum Alliance (https://www.scrumalliance.org/community/articles/2013/june/the-kanban-sandwich-a-bite-size-recipe-for-agile-w)
6. Gary Lister – Project Management Roots and Understanding the PMBOK Guide (FT Press – Pearson) (http://www.ftpress.com/articles/article.aspx?p=2261742&seqNum=12)
7. Jon Slemmer (Joy Group) – Project Process and Management: Agile versus Waterfall (http://www.joygroup.nl/news/project-process-and-management-agile-vs-waterfall)
8. Jack Grabovski (MyMG) – Lean Thinking Project Management in Six Sigma and Agile Models (http://www.mymanagementguide.com/lean-thinking-project-management-six-sigma-agile-models/)
9. Scrum Master – The 'Old' Waterfall Method (http://www.agile-scrum-master-training.com/agile-project-management/)
10. Mahesh Singh (SwiftStream) – How do you use Kanban in a Fixed Duration / Fixed Cost Project (http://blog.digite.com/how-do-you-use-kanban-in-a-fixed-duration-fixed-cost-project/)
11. Chuck Cobb (Udemy) – Mastering Agile Project Management for Project Managers (https://www.udemy.com/agile-project-management-overview-for-project-managers/)
12. Andrew Stellman (Building Better Software) – A Learning Agile Question from a business analyst (http://www.stellman-greene.com/2015/11/19/a-question-from-a-business-analyst/)
13. http://www.slideshare.net/prwpmp/pm104-presentation-deck
14. Shanaka Nagasinghe - Impact of Agile Project Management Practices on Enhancing the IT Project Success in Sri Lanka (https://www.linkedin.com/pulse/impact-agile-project-management-practices-enhancing-nagasinghe-pmp-)
15. Sarjil (Pinterest) - Program and Project Management Board (https://www.pinterest.com/sarjil/program-and-project-management/)
16. Jose Garcia - Project Management in "Agile" Projects: How Project Managers Can Succeed (https://www.linkedin.com/pulse/product-management-agile-projects-how-managers-can-succeed-garcia?trk=prof-post)
17. Ravi Kumar (etechplus) – What is the Scrum Process Flow (http://www.etechpulse.com/2015/02/agile-scrum-process-sdlc.html)

Nurul Haszeli Ahmad

04th December 2015
